



DT180 - Explore Solutions That Enable an Agile Transition to SAP S/4HANA


Reiner Markheiser, Joerg Marenk, SAP

Public

Questions?

If you have questions during the session, please use the **Chat** of the Broadcasting platform.

We have our colleagues Evan Stoddard, Frank Kuehn and John Krakowski in the background for answering your questions.

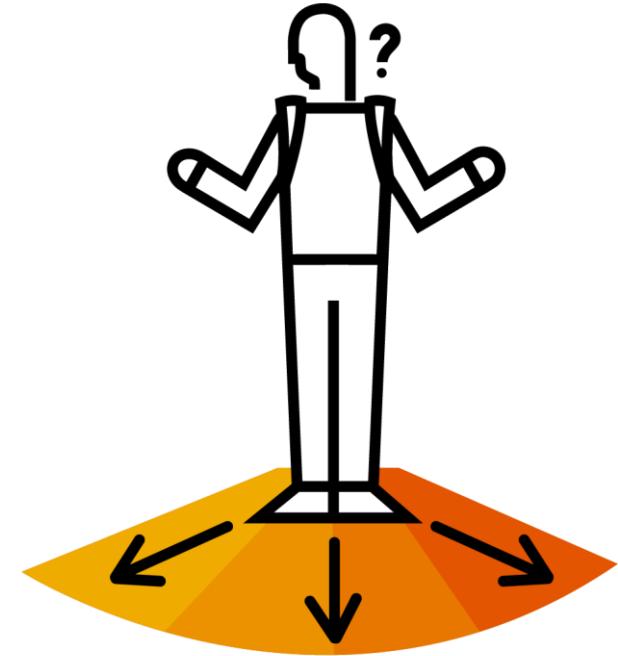

Important Information to our session



Exercise Information and System Access

Link to GitHub:

[DT180 – Explore Solutions That Enable an Agile Transition to SAP S/4HANA](#)

Agenda

SAP's ALM Offerings

SAP Solution Manager with Focused Build

- Architecture
- Reporting Capabilities
- Demos and Exercise

SAP Cloud ALM for Implementation

- Overview
- Capabilities
- End-to-End Implementation process and traceability
- Demos and Exercise

Where to find more Information

SAP's ALM Offerings



SAP's ALM Offerings

SAP Solution Manager

for hybrid solutions



The entire process from requirement to build, test, deploy, go-live, and run in an integrated methodology and tool set.

SAP Cloud ALM

available for multi cloud solutions



Implement cloud-centric solutions with a pre-configured, content-driven guided workspace based on SAP Activate methodology and Best Practices.

When to choose which ALM Solution?

Case 1: Customer has an on-premise-centric solution and plans to keep it.




Case 2: Customer has a cloud-centric solution or is cloud only.



Case 3: Customer has a small, standard on-premise solution.



Case 4: Customer moves to cloud or standardized ALM.




SAP ALM Platforms – Planned Product Availability Strategy

SAP Solution Manager follows the maintenance strategy of the SAP Business Suite


- Extended maintenance for process management, test suite, change & release management and ITSM in SAP Solution Manager 7.2 is automatically included in the optional extended maintenance for the SAP Business Suite 7.
- SAP Solution Manager 7.2 is supported beyond 2030 – in customer specific maintenance*
- There are **no plans for further releases** after SAP Solution Manager 7.2

SAP Cloud ALM and SAP Focused Run are not dependent on the SAP Business Suite, allowing mainstream maintenance beyond 2030. SAP plans no new on premise products in the ALM portfolio.

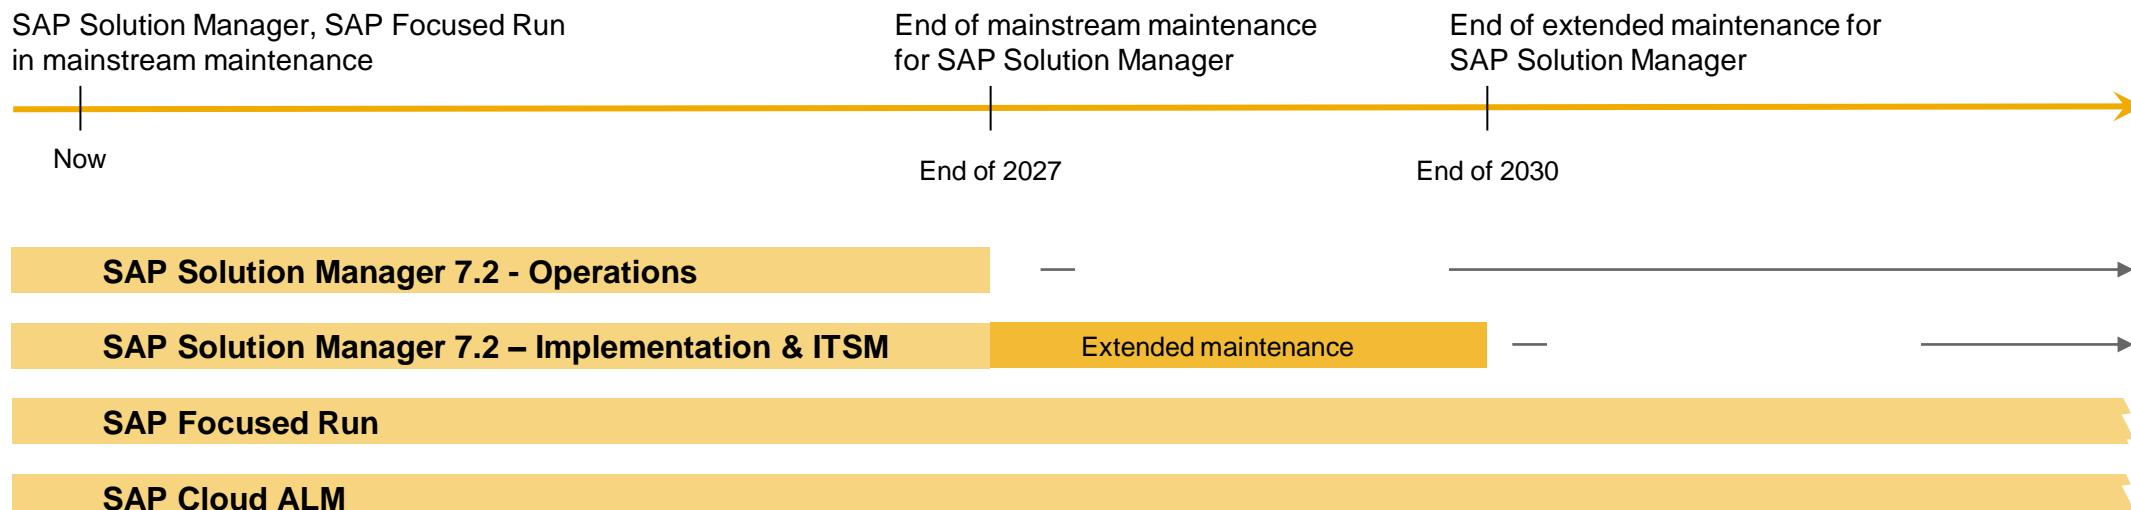

Transition Strategy from SAP Solution Manager to SAP Cloud ALM

SAP Cloud ALM is the Go-to platform for ALL new customers and over time ALL SAP Solution Manager customers.



Adopt SAP Cloud ALM for service and operations **NOW**

Reasons for immediate action

- Less customer effort for updates and agent administration
- Ease of use and consumption
- Functional enhancements for cloud products
- Access to the Service and Support network with data lake, ML and AI integration

Adopt SAP Cloud ALM for implementation **at your own pace**

Continue to use SAP Solution Manager to complete your move to SAP S/4HANA or if SAP Cloud ALM for implementation is not sufficient (yet)




- Standard functionality for Test, Change Control & Solution Documentation with daily delivery throughout 2023
- Advanced functionality for Charm & Solution Documentation later and with Partner functionality

Use SAP Cloud ALM for fast pace cloud implementations


SAP Solution Manager with Focused Build



SAP Solution Manager – Happy customers

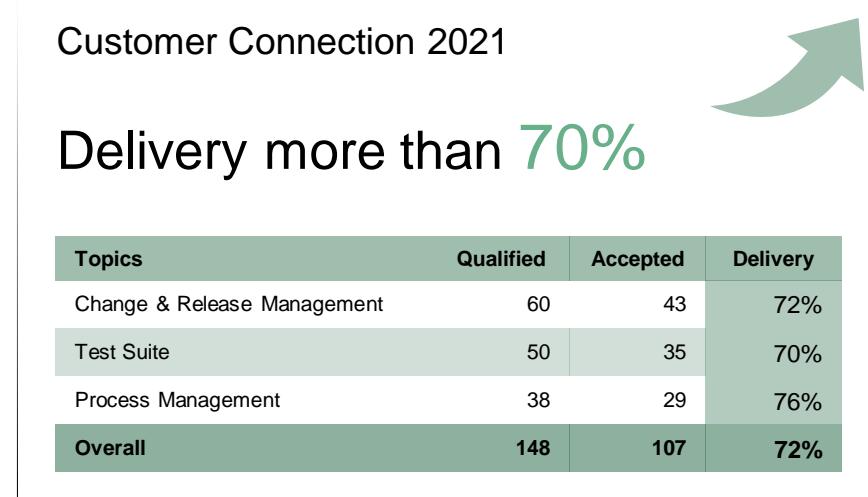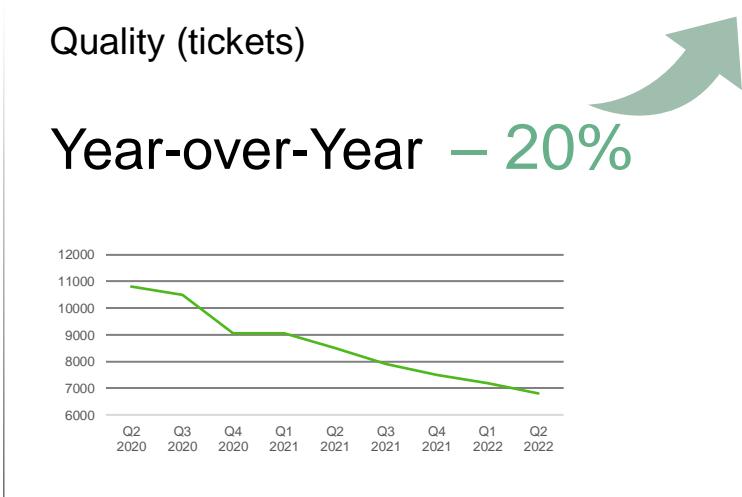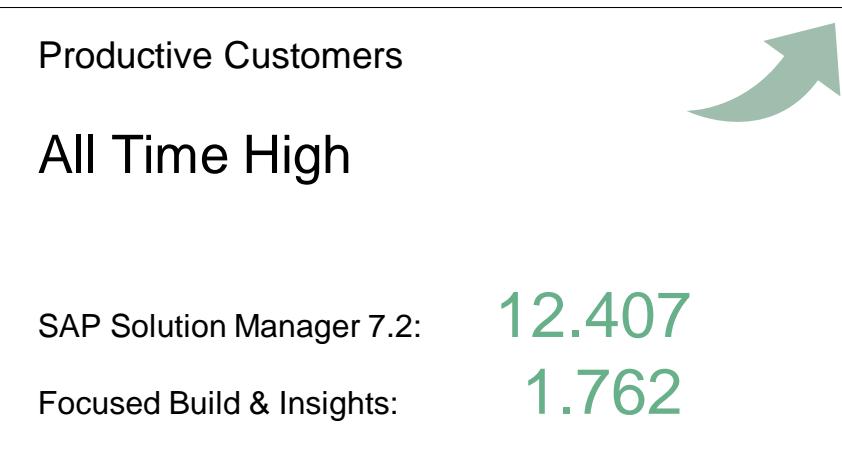


Focused Build – Architecture Overview and Integration Model

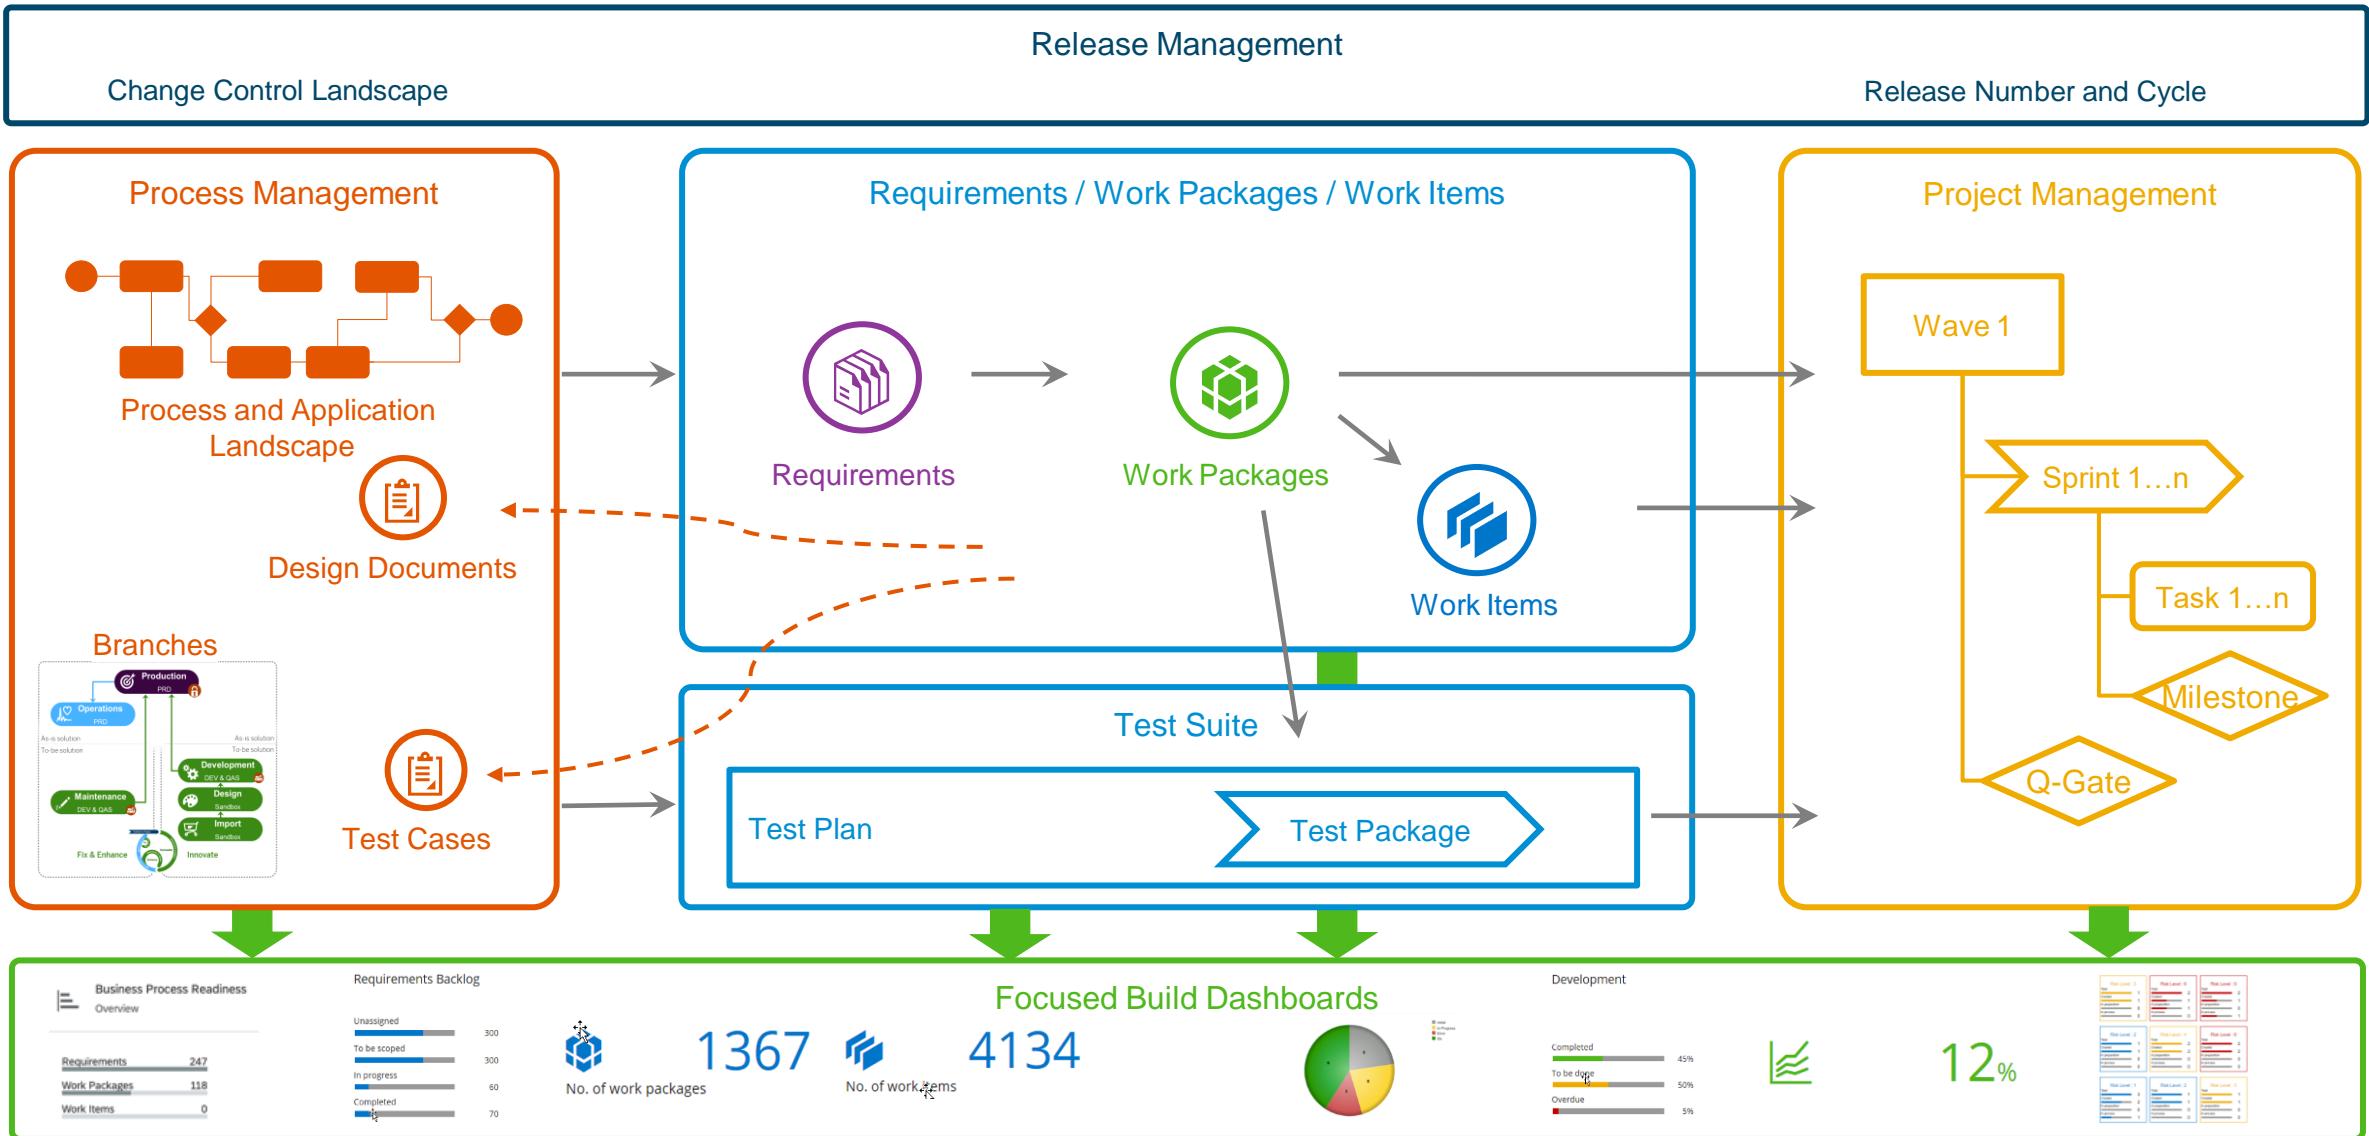




Focused Build Methodology

Standard Workflow

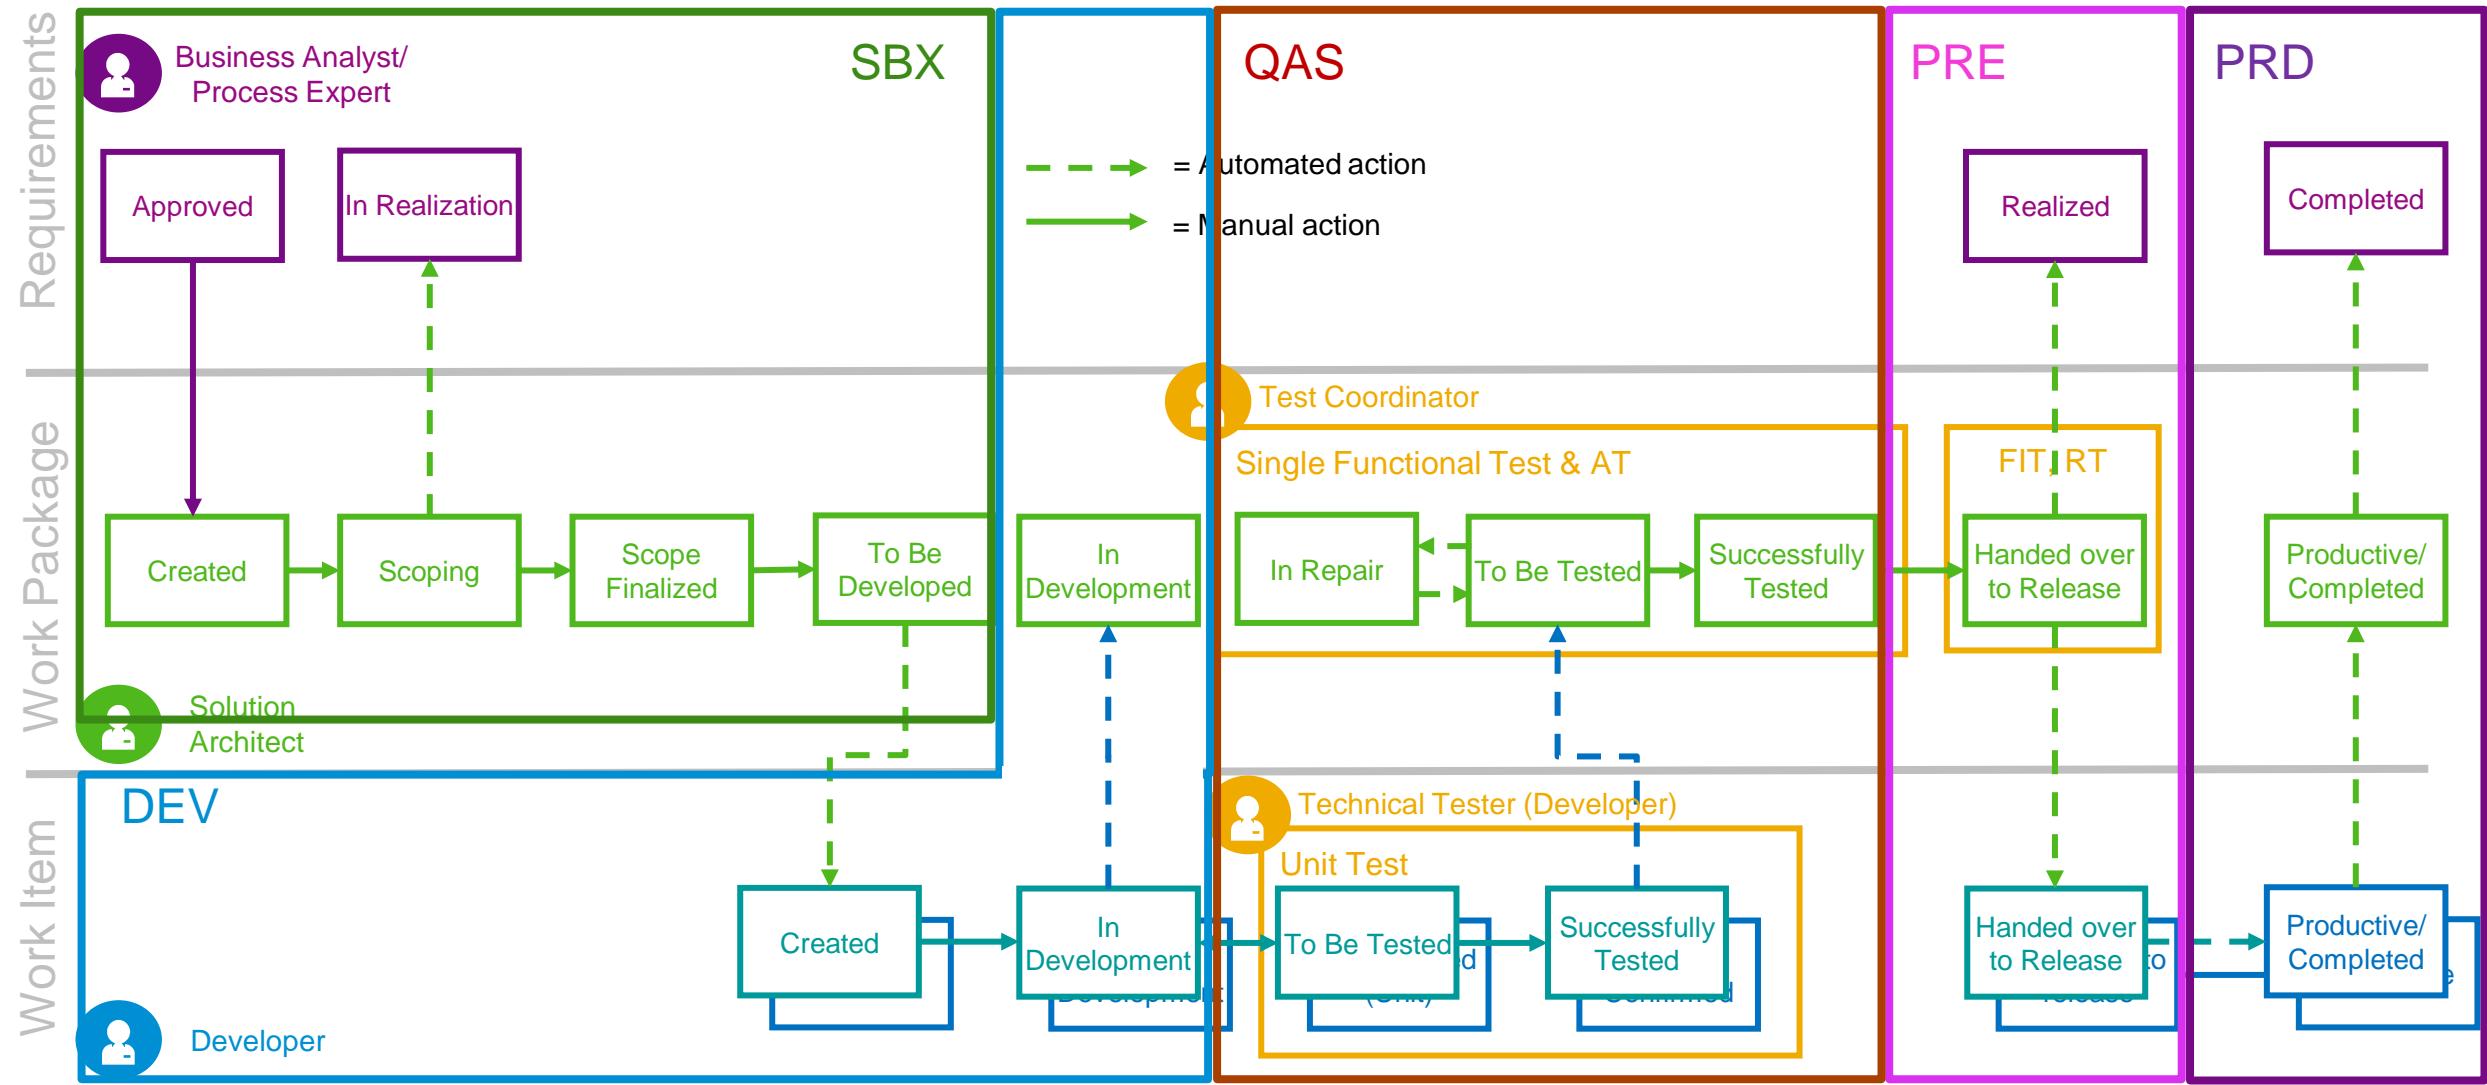

Available Dashboards in Focused Build

1/2

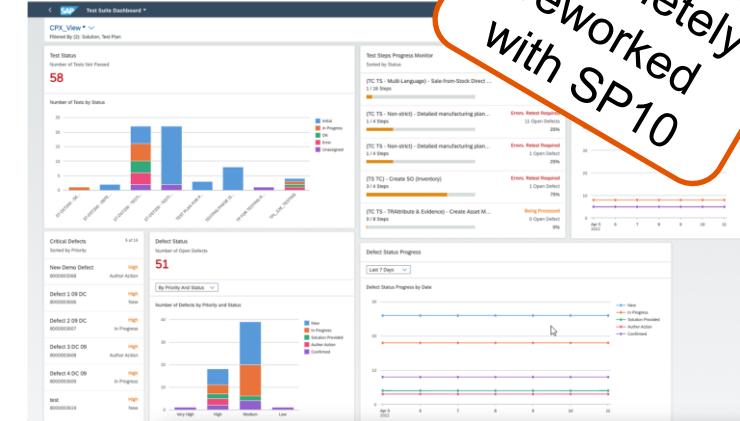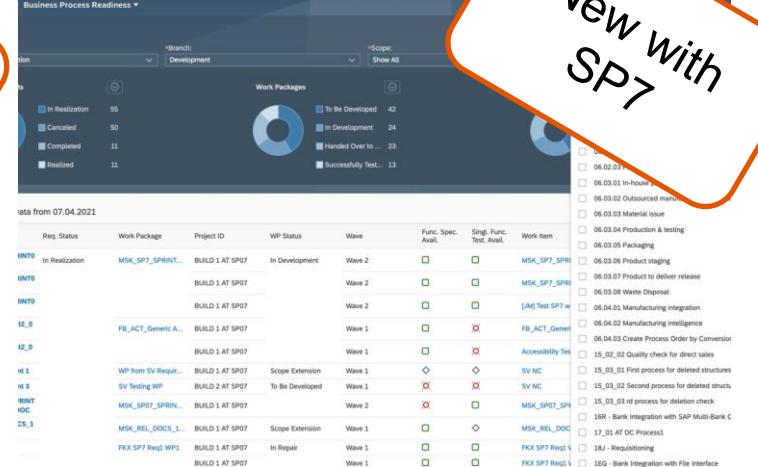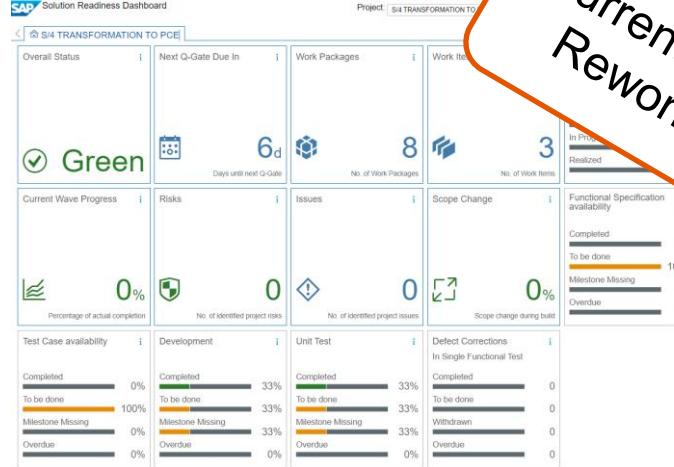

Solution Readiness Dashboard

- Gain an overview about the status of your project
- Provides information about completed, open and overdue SAP Activate project tasks
- Check for overdue KPIs

Document Reporting Dashboard



- Shows current status of implementation from business process perspective
- Executable for different branches (overview about planned, active and finished implementation activities for a certain documentation scope or specific business process)

Test Suite Dashboard

- Get an overview about the current testing phase
- Different Cards available for critical defects, Critical Test Executions, Test Status Progress etc.
- Detail Pages allow a deep dive into more granular information

Available Dashboards in Focused Build

2/2

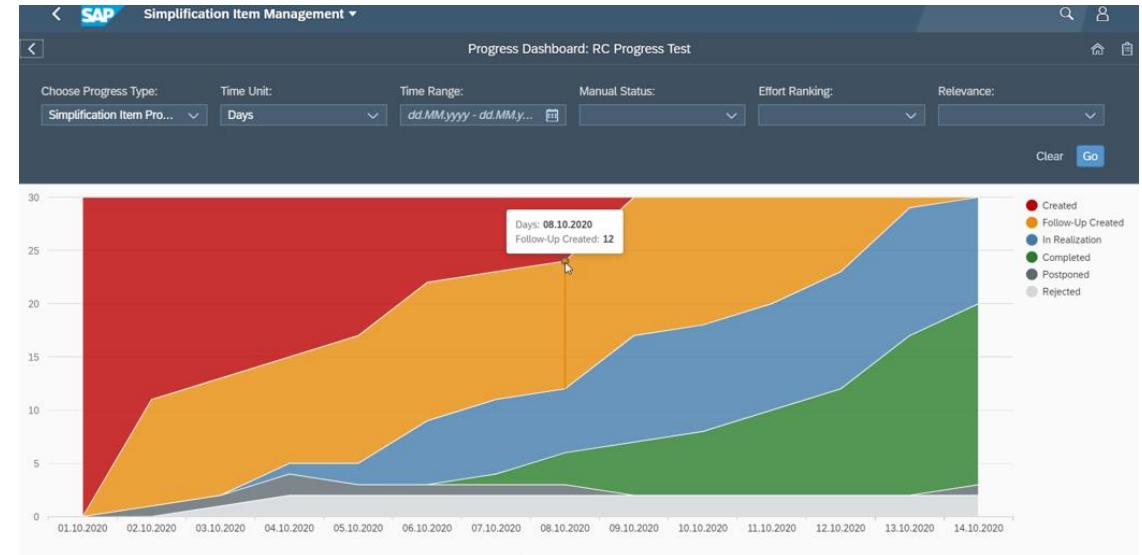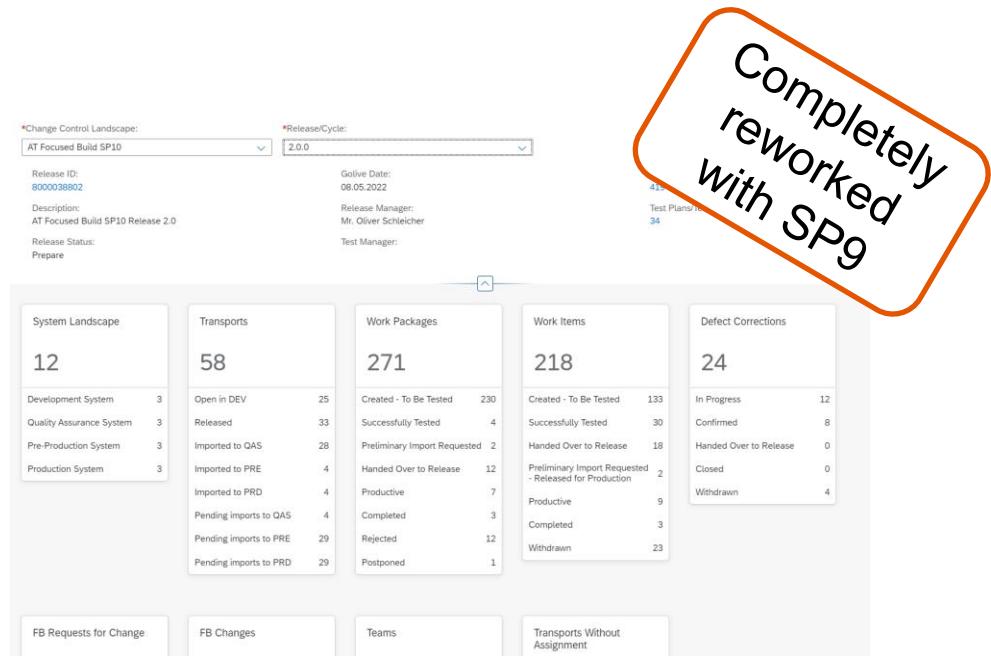

Release Dashboard

- Predefined queries allow a quick identification for Release Managers or System Administrators about ongoing transport activities for a Release
- Detail Pages show different ratings for selected items (for example Work Packages or Work Items) to ensure proper documentation, testing and transportation

Progress Dashboard for Readiness Check Integration


- Powerful Burndown-Chart for Simplification Items and Conversion Activities
- Shows the progress of performed conversion steps over a certain period
- Allows filtering to focus on most important Activities

Test Suite – new with SP10

New version of Test Suite Dashboard

Description

With ST-OST SP10, a new version of the Test Suite Dashboard is delivered, using standard Fiori elements. It offers a unique way to analyze data step by step from different perspectives, to investigate a root cause through drilldown, and to act on transactional content.



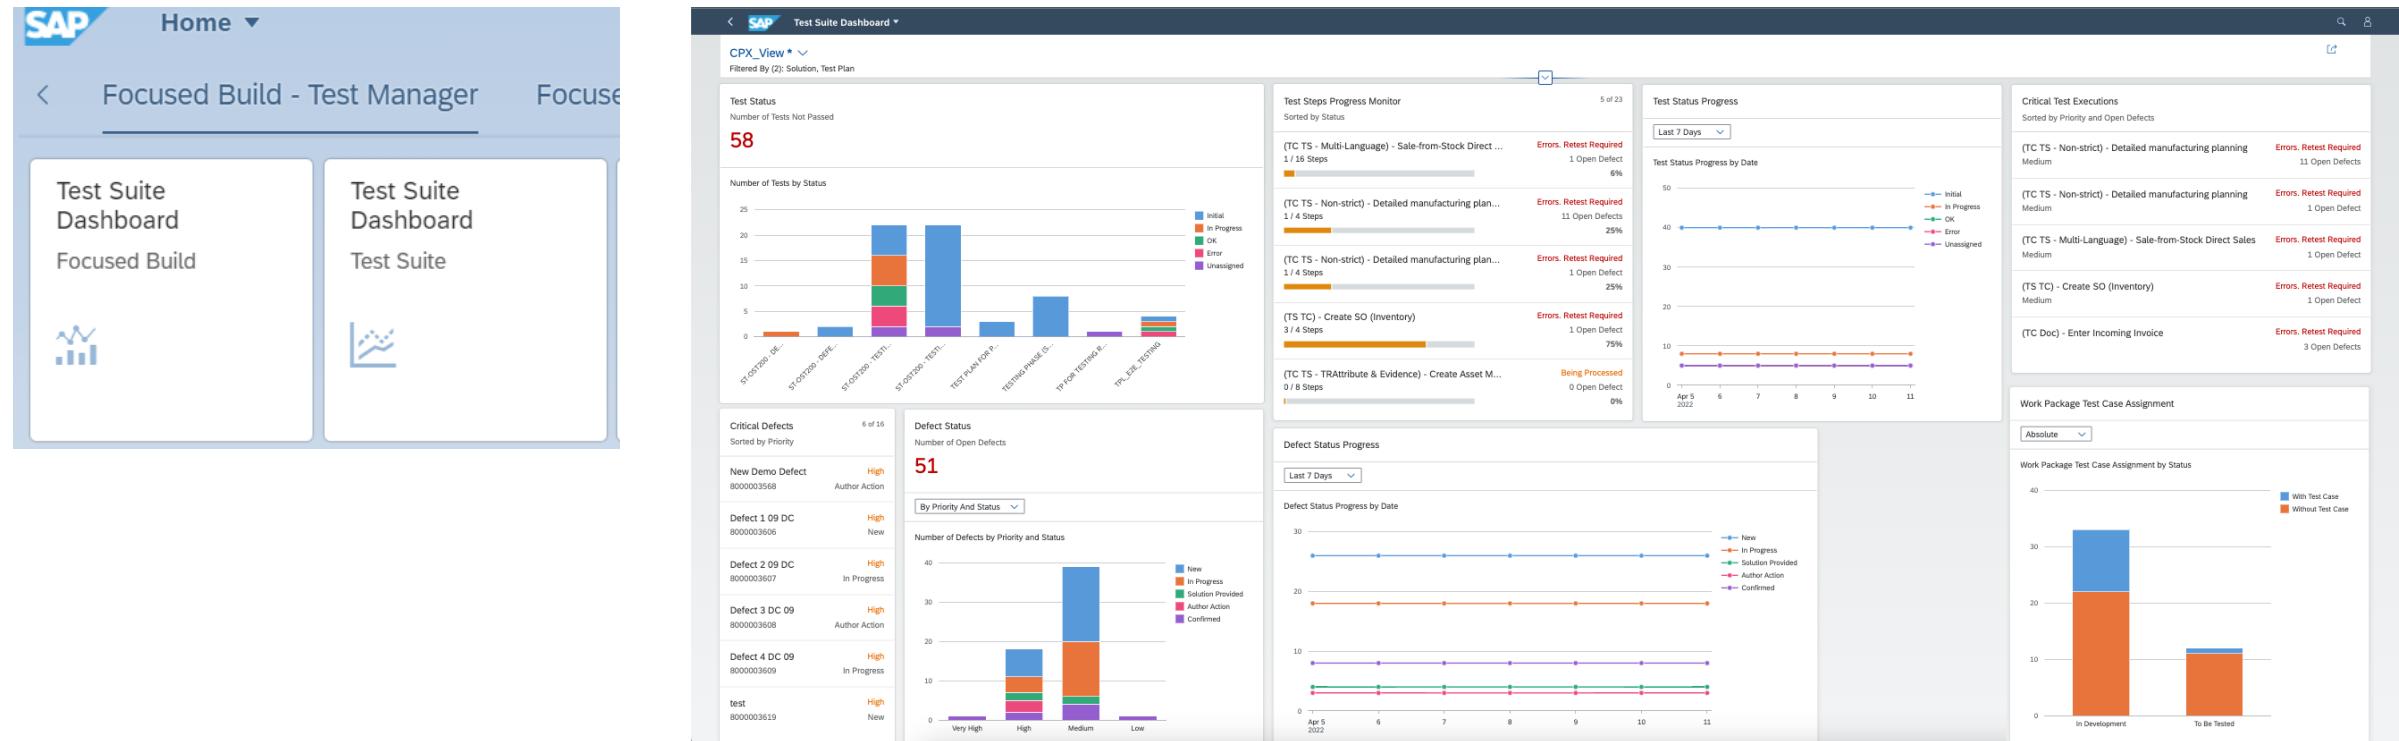





Customer Connection

General Capabilities

- Adaptable Overview Pages
- Interactive Detail Pages
- Easy Creation of Page variants that can be shared
- Configurable Chart Visualizations
- Tabular data display including reordering and grouping
- View by different dimensions
- Possibility to download the detailed data
- Easily manage the visibility of cards
- Share using email or URL, and Save as Tile

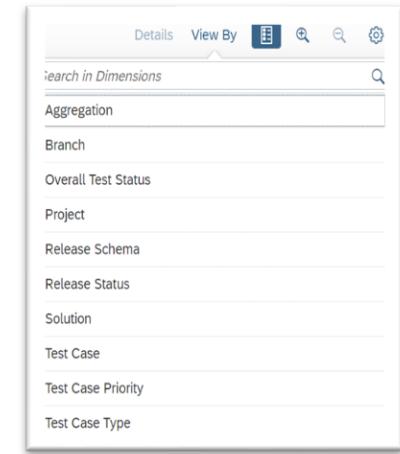


Data aggregated by: test1.xlsx								
A	B	C	D	E	F	G	H	
Test Plan	# Test Cases	# Unassigned	# Initial	# In Progress	# OK	# Error	# Open Defects	Test Plan A
FB RelDash Test Plan Sp09 (FB REL)	20	6	6	2	3	3	3	19




Navigation Paradigm in Test Suite Dashboard

This screenshot shows the navigation paradigm within a dashboard titled 'Musta_TestStatus_Overview1*'. It includes dropdown menus for 'Solution' (AT FB SP11 Solution), 'Project' (FB RELDASH TEST PLAN SP09), 'Test Plan' (TM_TS_MAS), and 'Test Package'.


Filter and Variant Management

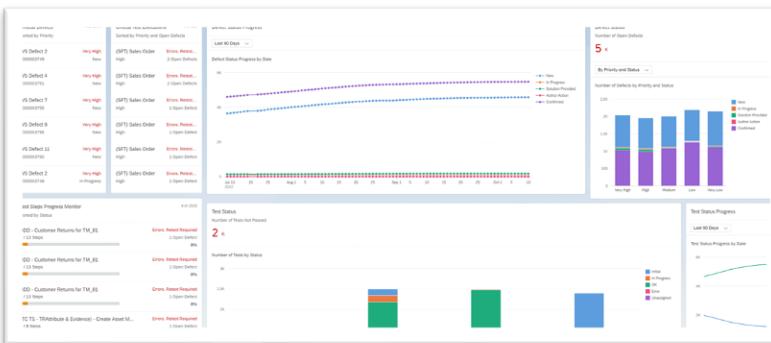

Overview Page with
different Cards

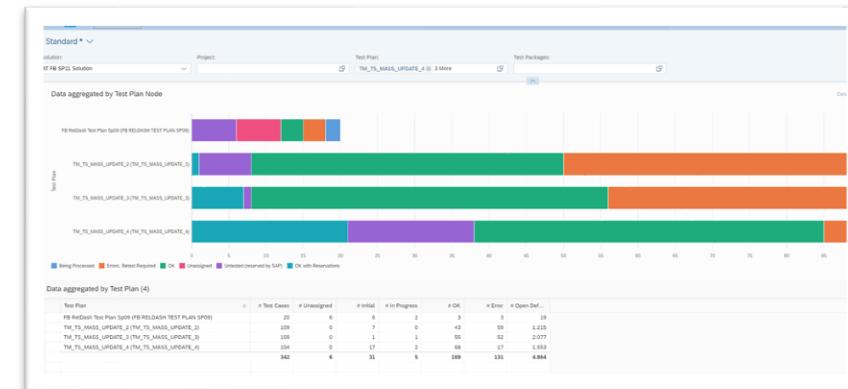

Detail Pages






Demo

Test Suite Dashboard Capabilities


Release Dashboard in Focused Build – released with SP09

New User Interface for Release Dashboard

- Drill down from top level dimensions down to the transport request level
- Breadcrumb navigation to show current context
- Filter options for work packages, work items, defect corrections, FB requests for change, FB changes and transport requests
- Status ratings to evaluate the completeness of releases
- Control of pending imports of transport requests

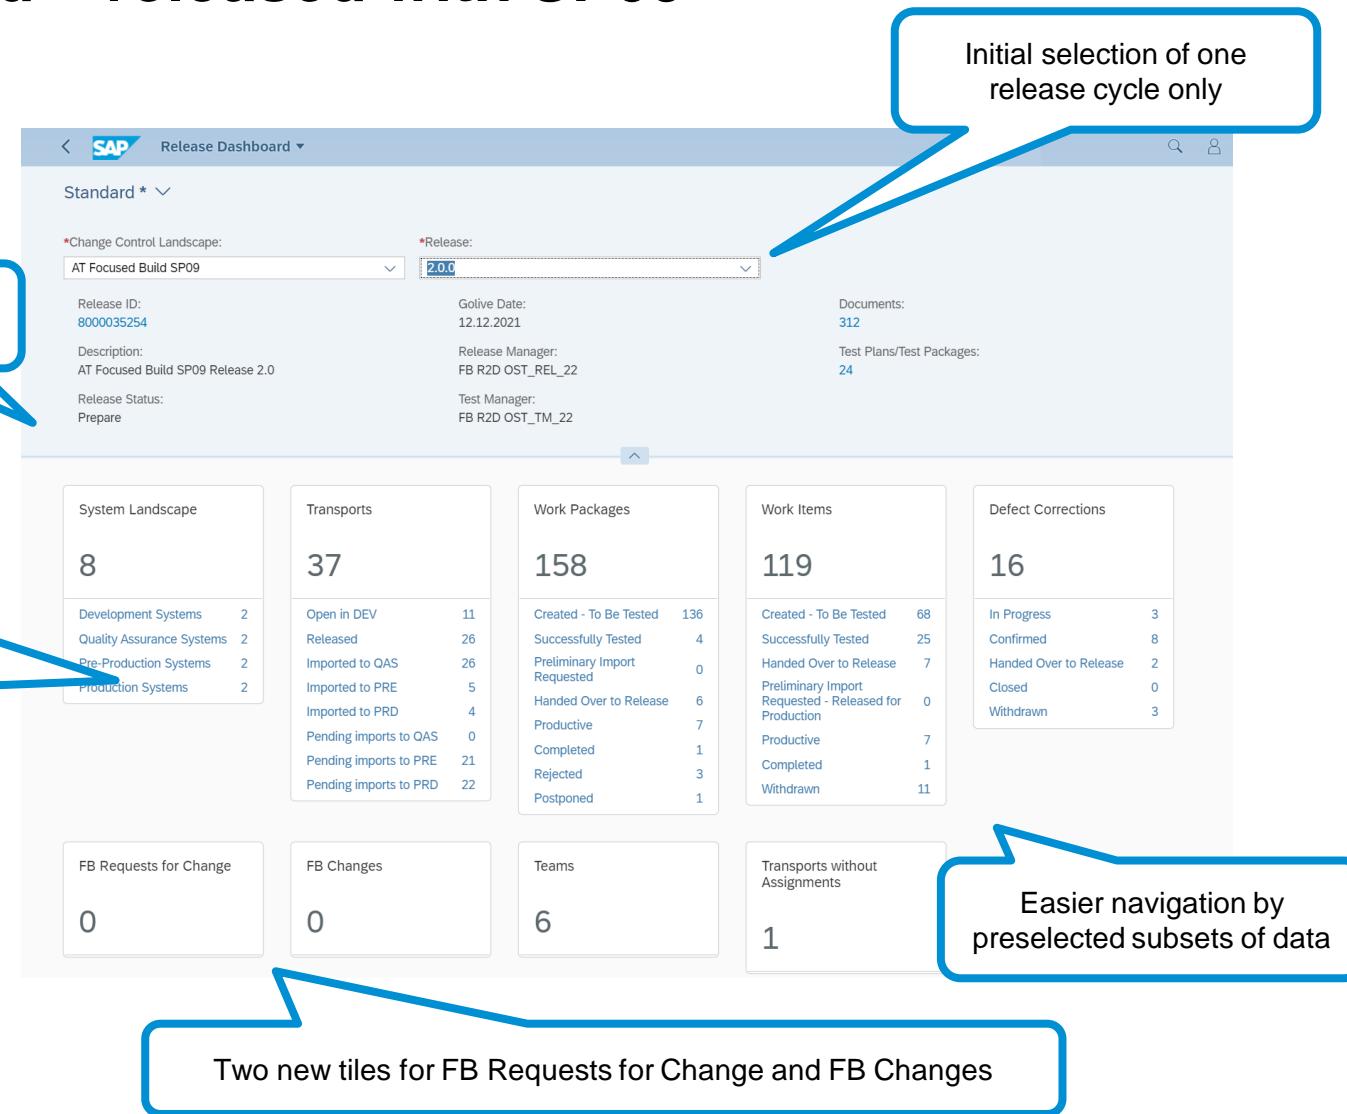

Exercise Preparation: Acceptance Test Evaluation and Functional Integration Test / Deployment Preparation

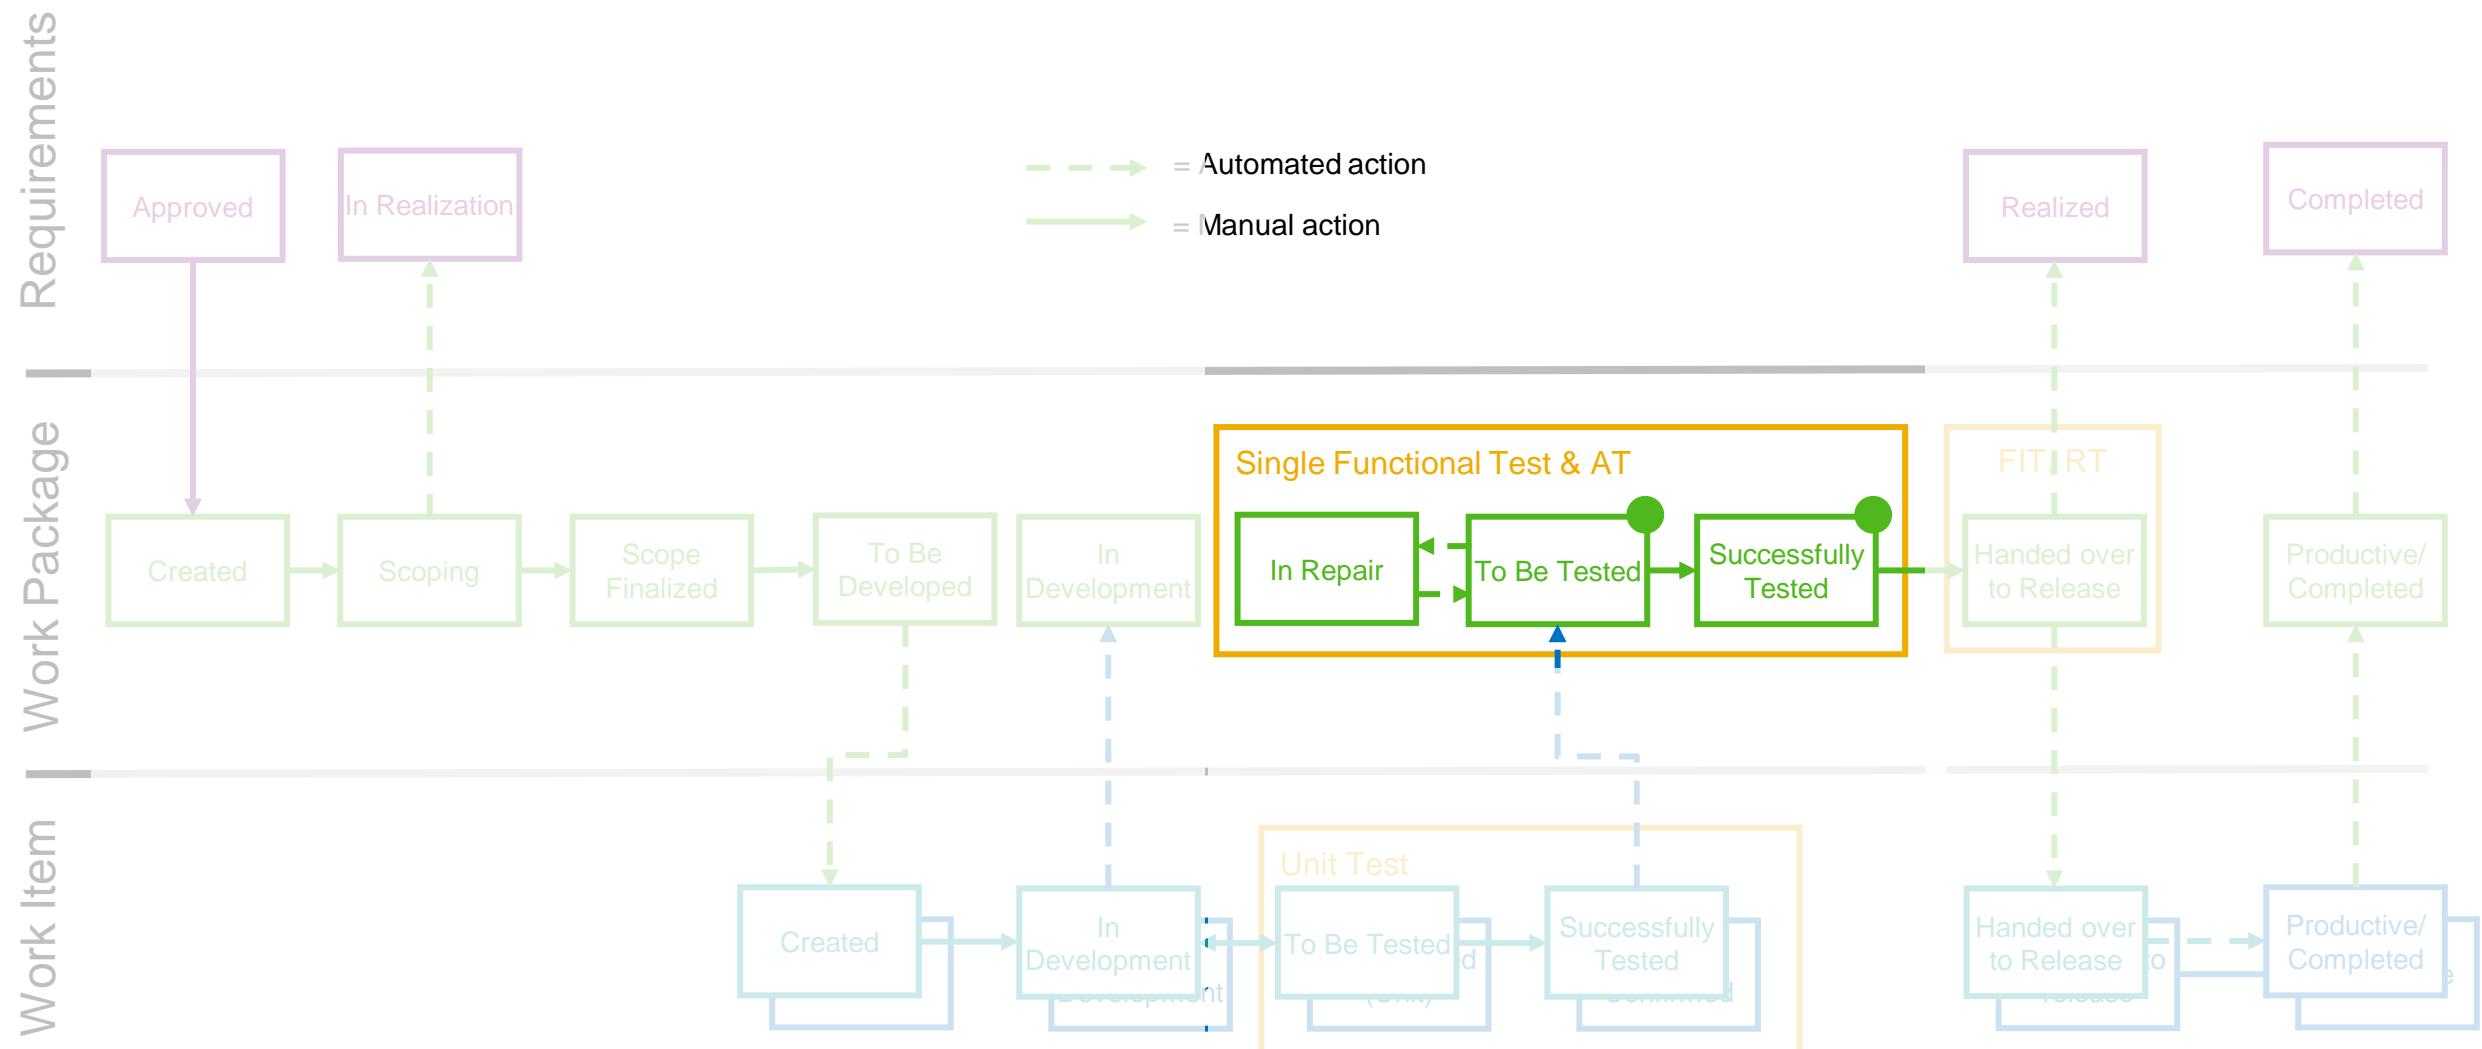

Test Plan Management – Assignment Analysis

Assignment Analysis and Test Plan Generation Work Packages without Test Plan Coverage

Test Plan ID: [TPL_DT180-00_20221107_091502](#) Description: Acceptance Test Conversion Project Wave 1 Test Classification: Acceptance Test

Select Change Document ▾ Development ▾

Test Case Selection Test Package Details

Test Packages

View: [Standard View] ▾ | Print Version | Export ▾ | Collapse Test Case Level | Assign Testers | Update Work Packages |

<input type="checkbox"/> Test Package ...	Description	Perso...	Plann...	Plann...	Work ...	Work ...	Work ...	Requi...	Requi...	Test Case	Over...	Test ...
<input type="checkbox"/> 8000013378	S4TWL - JOB SCHEDULI...	Agatha ...	31.10.2...	11.11.2...	800001...	S4TWL ...	To Be T...			E2E_OTC_Sale-from-Sto...	■	
<input type="checkbox"/> 8000013379	S4TWL - JOB SCHEDULI...	Agatha ...	31.10.2...	11.11.2...	800001...	S4TWL ...	To Be T...			E2E_OTC_Sale-from-Sto...	■	
<input type="checkbox"/> 8000013383	S4TWL - Planning Horizon	Agatha ...	31.10.2...	11.11.2...	800001...	S4TWL ...	To Be T...			OSAP_30_Sales Order En...	▲	
<input type="checkbox"/> 8000019143	ABAPTWL - AS Java not ...	Agatha ...	31.10.2...	11.11.2...	800001...	ABAPTL...	To Be T...			OSAP_30_Sales Order En...	▲	
<input type="checkbox"/> 8000019145	ABAPTWL - Cleanup of o...	Agatha ...	31.10.2...	11.11.2...	800001...	ABAPTL...	To Be T...			OSAP_30_Create Sales O...	■	
<input type="checkbox"/> 8000019150	S4TWL - Amount Field Le...	Agatha ...	31.10.2...	11.11.2...	800001...	S4TWL ...	To Be T...			OSAP_30_Review Sales ...	■	
<input type="checkbox"/> 8000019151	S4TWL - Amount Field Le...	Agatha ...	31.10.2...	11.11.2...	800001...	S4TWL ...	Succes...			OSAP_30_Sales Order En...	■	
<input type="checkbox"/> 8000019157	S4TWL - Globalization – ...	Agatha ...	31.10.2...	11.11.2...	800001...	S4TWL ...	In Deve...			OSAP_30_Billing	■	
<input type="checkbox"/> 8000019158	S4TWL - Reporting/Analyt...	Agatha ...	31.10.2...	11.11.2...	800001...	S4TWL ...	In Deve...			OSAP_30_Create Sales O...	▲	

Selection Criteria

- Test Plan for Acceptance Test
- Expanded Test Case Level

Action to be performed

- Select Work Packages where Overall Test Status is green
- Update selected Work Packages by changing the status to “Successfully tested”

Release Dashboard – Check Readiness for Functional Integration Test

Home / AT Focused Build SP10 Release 2.0 > Work Packages

Work Packages

Status: System: System Role: Rating: Development Team: Test Team: Adapt Filters (1) Go

2 Items

Rating	Object ID	Description	Priority	Rating Documents	Rating Tests	Rating Transports	Status	Development Team	Test Team	Work Items	Documents	Tests	Transports	Defect Corrections
<input type="checkbox"/>	8000039617	S4TWL - Manage General Ledger Transfer	4: Low	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Successfully Tested			1	3	1	0	0
<input type="checkbox"/>	8000039637	xx_49_DropDocs	4: Low	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Successfully Tested			1	6	0	2	1
<input type="checkbox"/>	8000039966	WP_OST_50_TST_REL_DASH	3: Medium	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Successfully Tested			1	0	0	1	1
<input type="checkbox"/>	8000039690	SP10_BR_0421_will01	2: High	<input type="checkbox"/>	<input type="checkbox"/>	<input checked="" type="checkbox"/>	Successfully Tested	Development Team 1		1	4	0	0	0

Selection Criteria

- Work Package Status = Successfully Tested
- Rating Documents = Green
- Rating Tests = Green
- Rating Transports = Green

Action to be performed

- Select Work Packages that fulfill these criteria and navigate to Mass Change Application
- Change status of selected Work Packages to “Handed over to Release”
- Navigate to Release Batch Import Trigger application and schedule import to Preproduction System



Demo

Check for Acceptance Test Readiness and Completion in Assignment Analysis
Check for Readiness of Release for Functional Integration Test & Prepare Go-Live in Release Dashboard



Exercise

Check for Acceptance Test Readiness and Completion in Assignment Analysis
Check for Readiness of Release for Functional Integration Test & Prepare Go-Live in Release Dashboard

Integration to SAP Analytics Cloud

Features:

- Collection report available to regularly move data to SAP Analytics Cloud
- Covers the whole Requirements-to-Deploy process including Requirements, Work Packages, Work Items and Test Suite Data
- Customers can create their own dashboards tailored to their specific needs
- API documentation available in SAP API Hub:
<https://api.sap.com/api/SAC/overview>



Note: SAP Analytics Cloud is an optional Scenario and requires SAP Analytics Cloud subscription

New Solution Readiness Dashboard




Lab Preview

Solution Readiness Dashboard

A new version of the Solution Readiness Dashboard is being built, using standard Fiori elements.

Provides the possibility to analyze data step by step from different perspectives, to investigate a root cause through drilldown, and to act on transactional content.

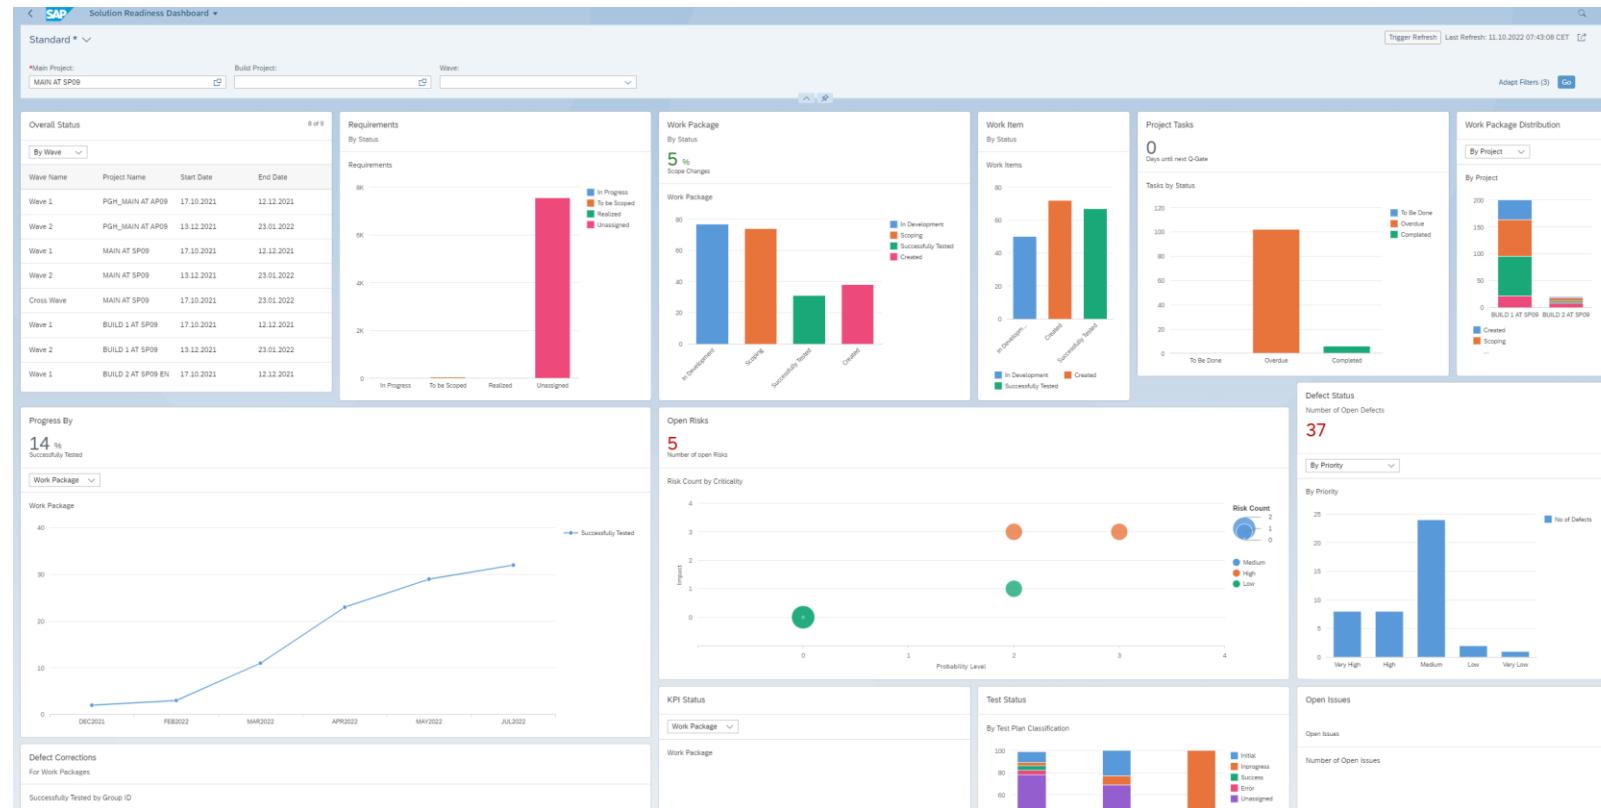

This is the current state of planning and may be changed by SAP at any time.

General Capabilities


- Adaptable Overview Pages
- Easy Creation of Page variants that can be shared
- Configurable Chart Visualizations
- Tabular data display including reordering and grouping
- View by different dimensions
- Possibility to download the detailed data
- Easily manage the visibility of cards
- Share using email or URL, and Save as Tile

The screenshot shows a Fiori application interface. On the left, a 'Manage Cards' dialog lists various items with toggle switches: Overall Status (off), Requirements (off), Work Package (on), Work Item (off), Project Tasks (off), Work Package Distribution (off), Work Item Distribution (off), and Defect Corrections (on). Below these is a 'Progress By' section with 'OK', 'Reset', and 'Cancel' buttons. To the right, a 'View By' section includes a search bar for 'Dimensions' and a dropdown menu for 'Aggregation'. Further right is a 'Chart Types' section with a search bar and a list of 18 chart types: Bar Chart, Column Chart, Line Chart, Pie Chart, Donut Chart, Heat Map, Bullet Chart, Vertical Bullet Chart, Stacked Bar Chart, Stacked Column Chart, 100% Stacked Bar Chart, 100% Stacked Column Chart, Waterfall Chart, and Horizontal Waterfall Chart.

The screenshot shows a Fiori application interface with a header 'Last Refresh: 10.10.2022 21:38:47 CET' and a refresh icon. In the bottom right corner, there is a floating action bar with three buttons: 'Send E-Mail' (with an envelope icon), 'Save as Tile' (with a star and plus icon), and 'Adapt Filters (1)'.


Overview Page in Solution Readiness Dashboard

Different Cards and Usage

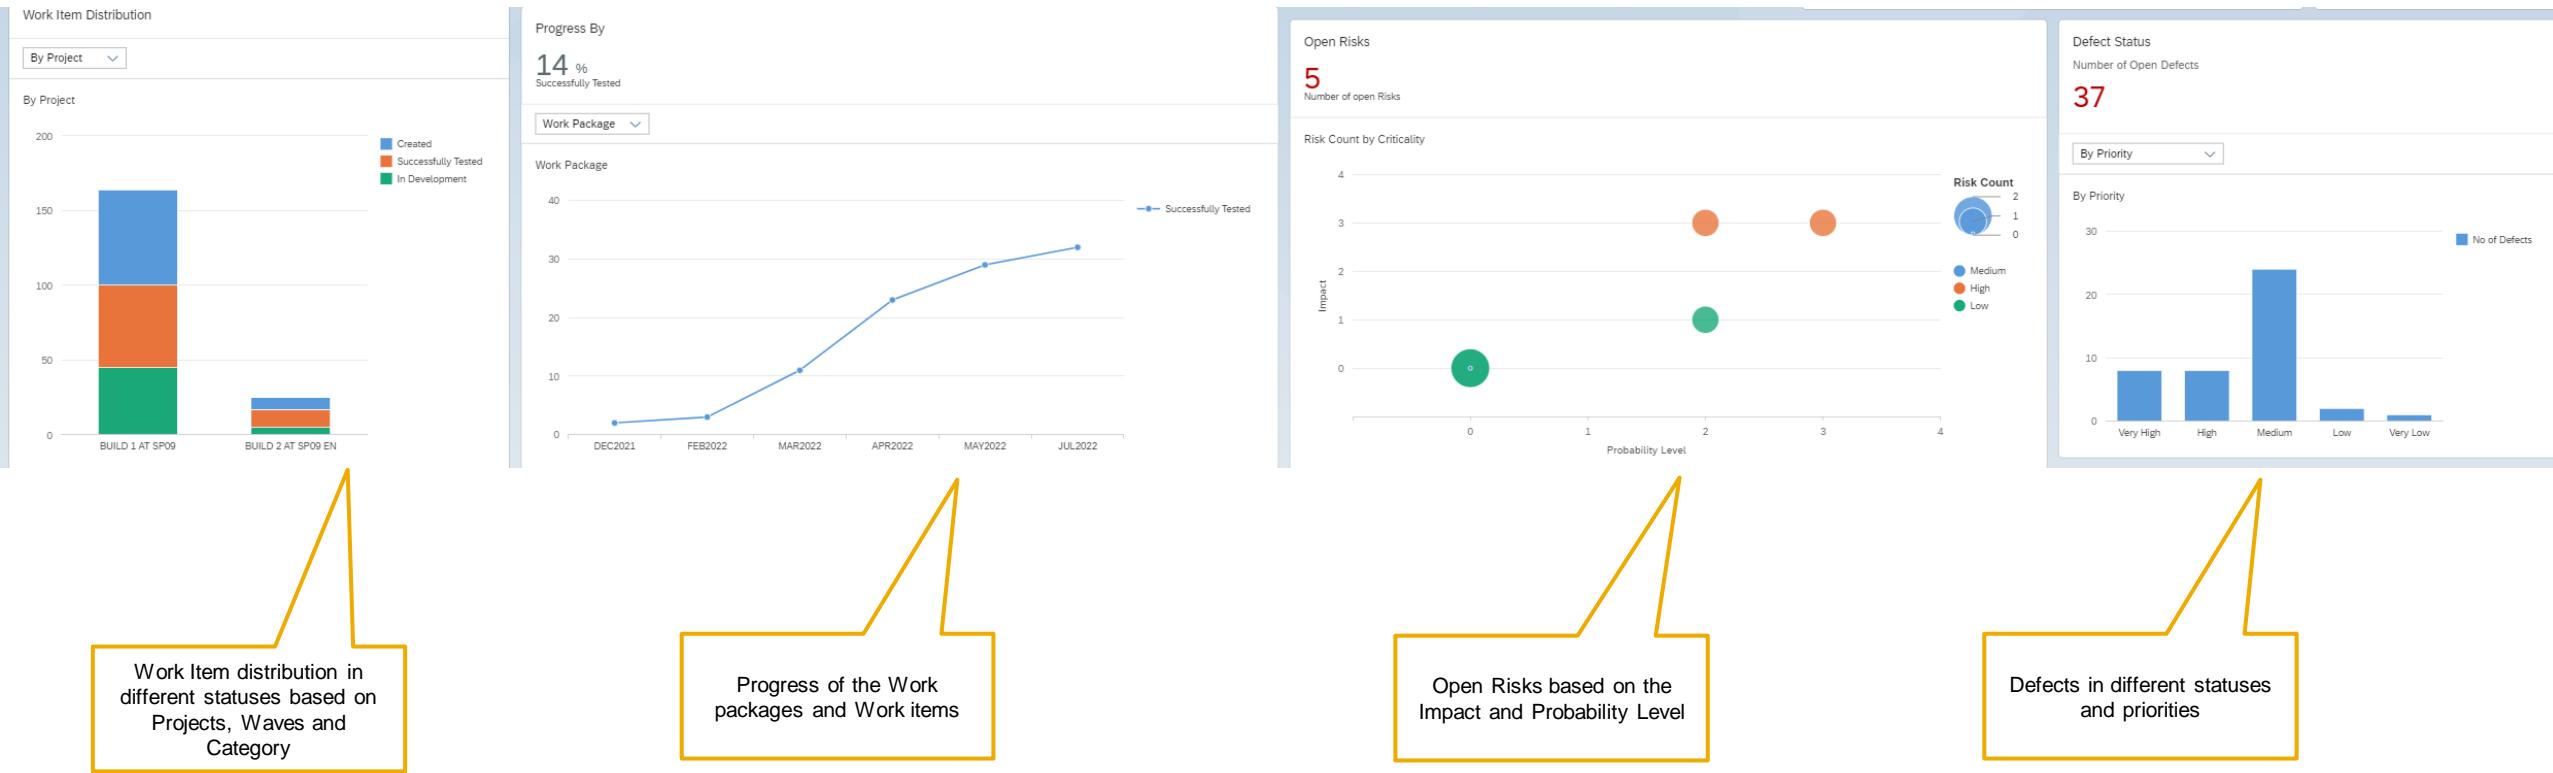

Overview Page in Solution Readiness Dashboard

Different Cards and Usage

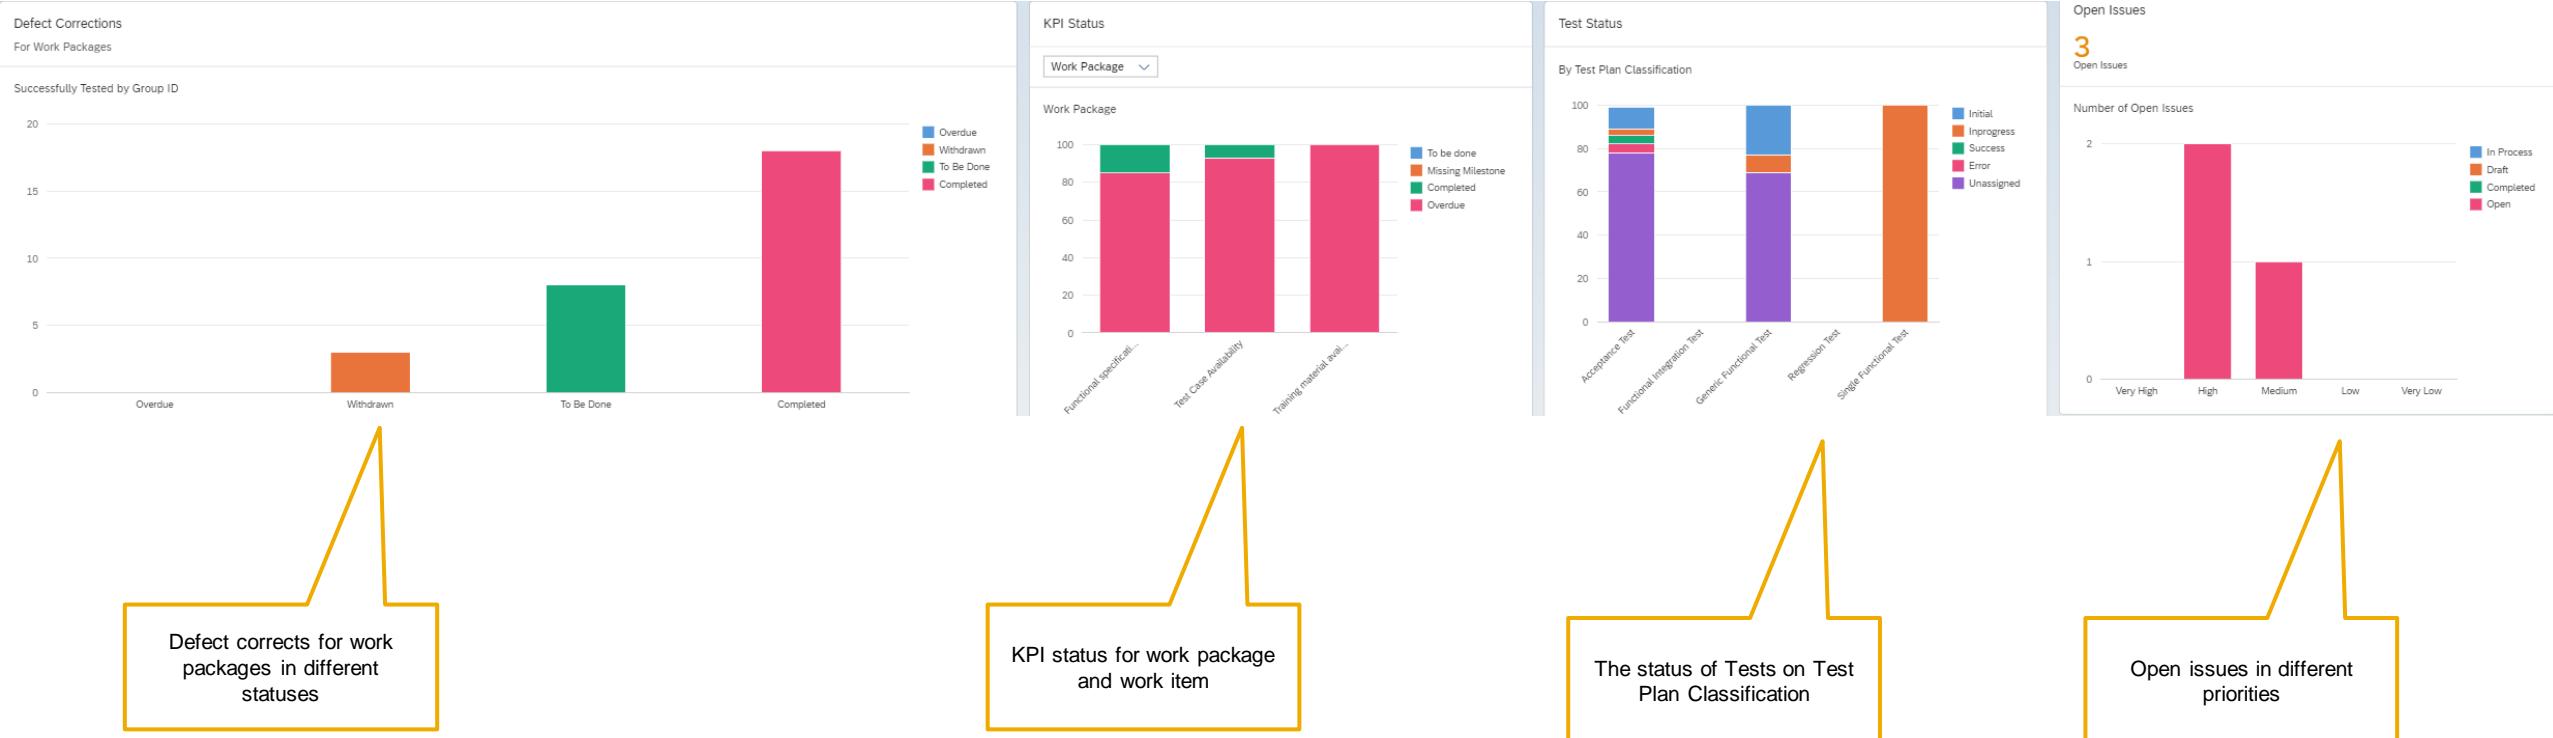



Demo


Lab Preview Solution Readiness Dashboard

SAP Cloud ALM for implementation




Introduction

SAP Cloud ALM provides the harmonized implementation experience for the intelligent enterprise, covering all relevant SAP solutions for all customers

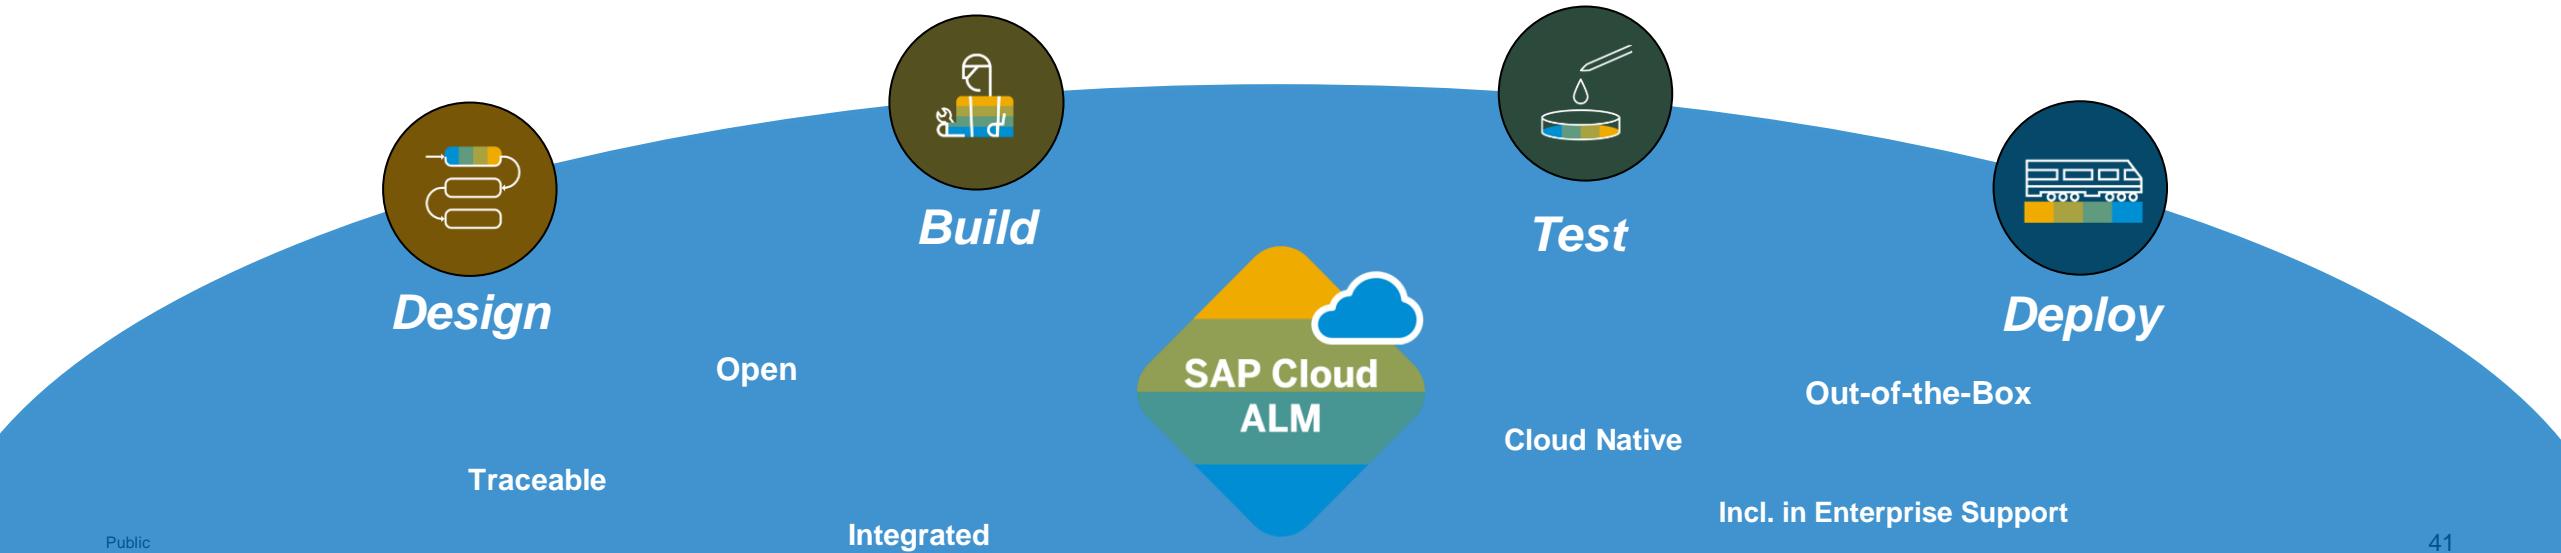

Introduction

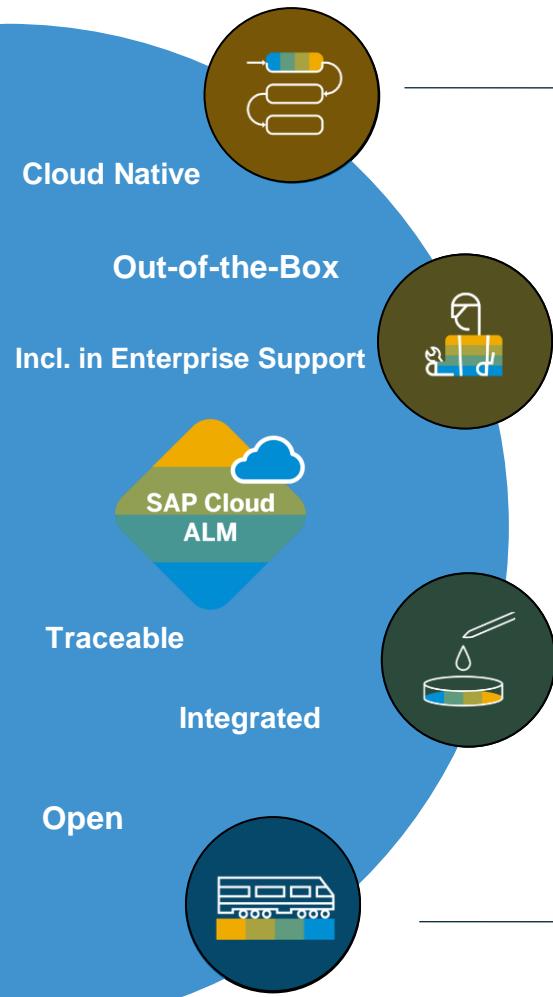

Design the to be solution

- Start with Best Practice Content to run your Fit-2-Standard workshops
- Create own processes with integrated authoring capabilities
- Collect requirements as an initial backlog

Manage all project activities

- Based on the SAP Activate methodology with template roadmaps for agile implementation projects
- Extended by your own tasks and user stories
- Integrated planning and reporting

Ensure Quality

- Manage all test from user acceptance to regression
- Manual testing with test step based approach
- Integration of automatic execution engines


Manage Successful Deployment & Go-Live

- Plan your releases and orchestrate consistent deployment to production
- Enable change and provide traceability and audit trails

High flexibility provided by SAP Cloud ALM


Free choice of used capabilities depending on

- Functional needs
- Implementation use case; e.g. S/4HANA Cloud, S/4HANA Private Cloud, Success Factors
- Integration of third party solutions

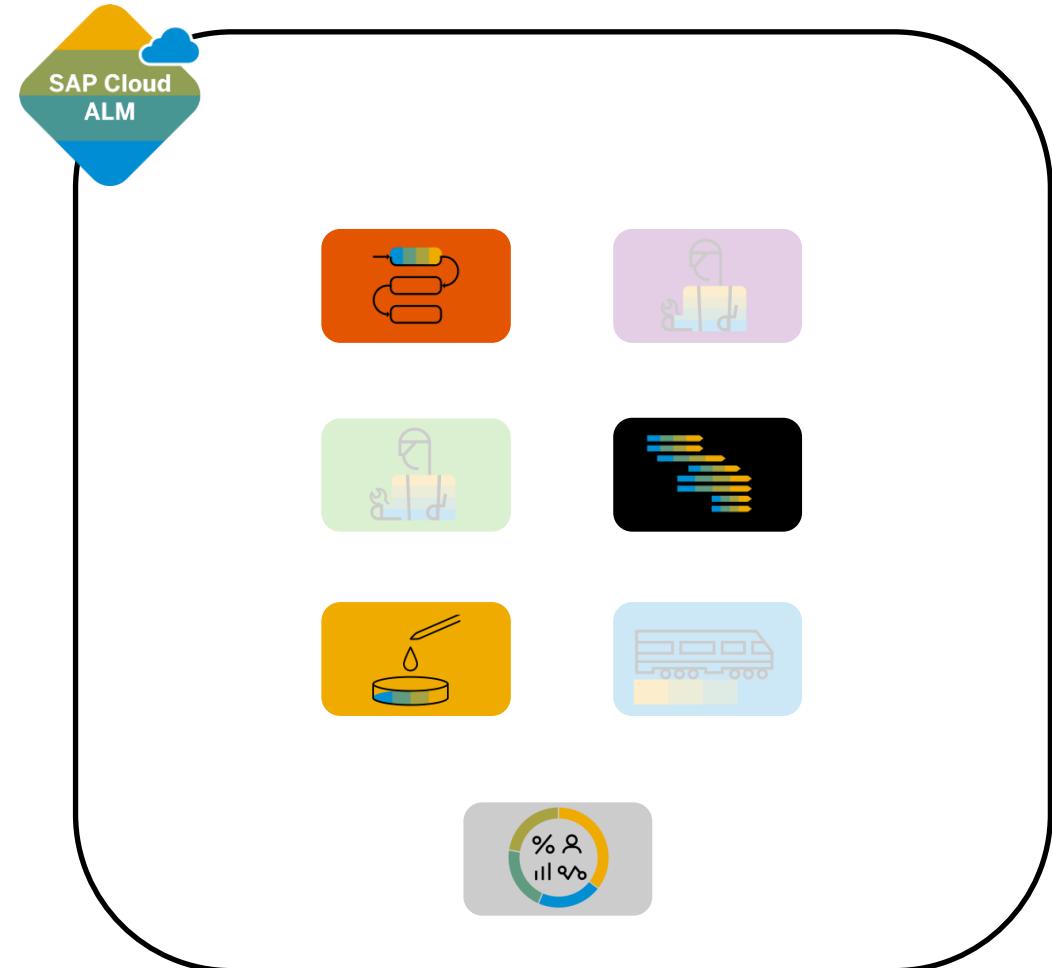


Maximum Value by using integrated E2E implementation process

- Utilize entity relations as basis for an integrated process
- Manage entity dependencies and implementation process governance via traceability views
 - Solution Process Traceability
 - Requirement Traceability
 - Feature Traceability
- Requirement driven implementation to support customer specific innovation

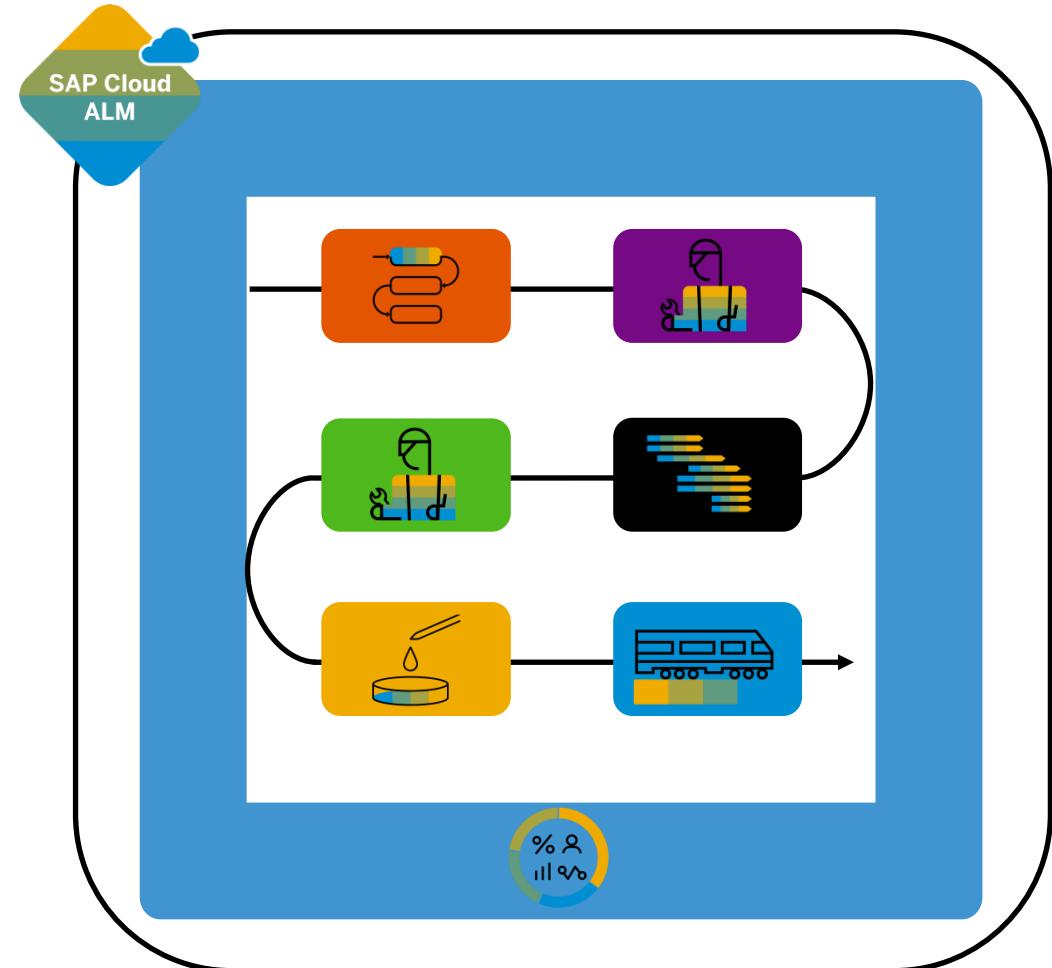


Requirement Driven Implementation

End-to-end implementation model

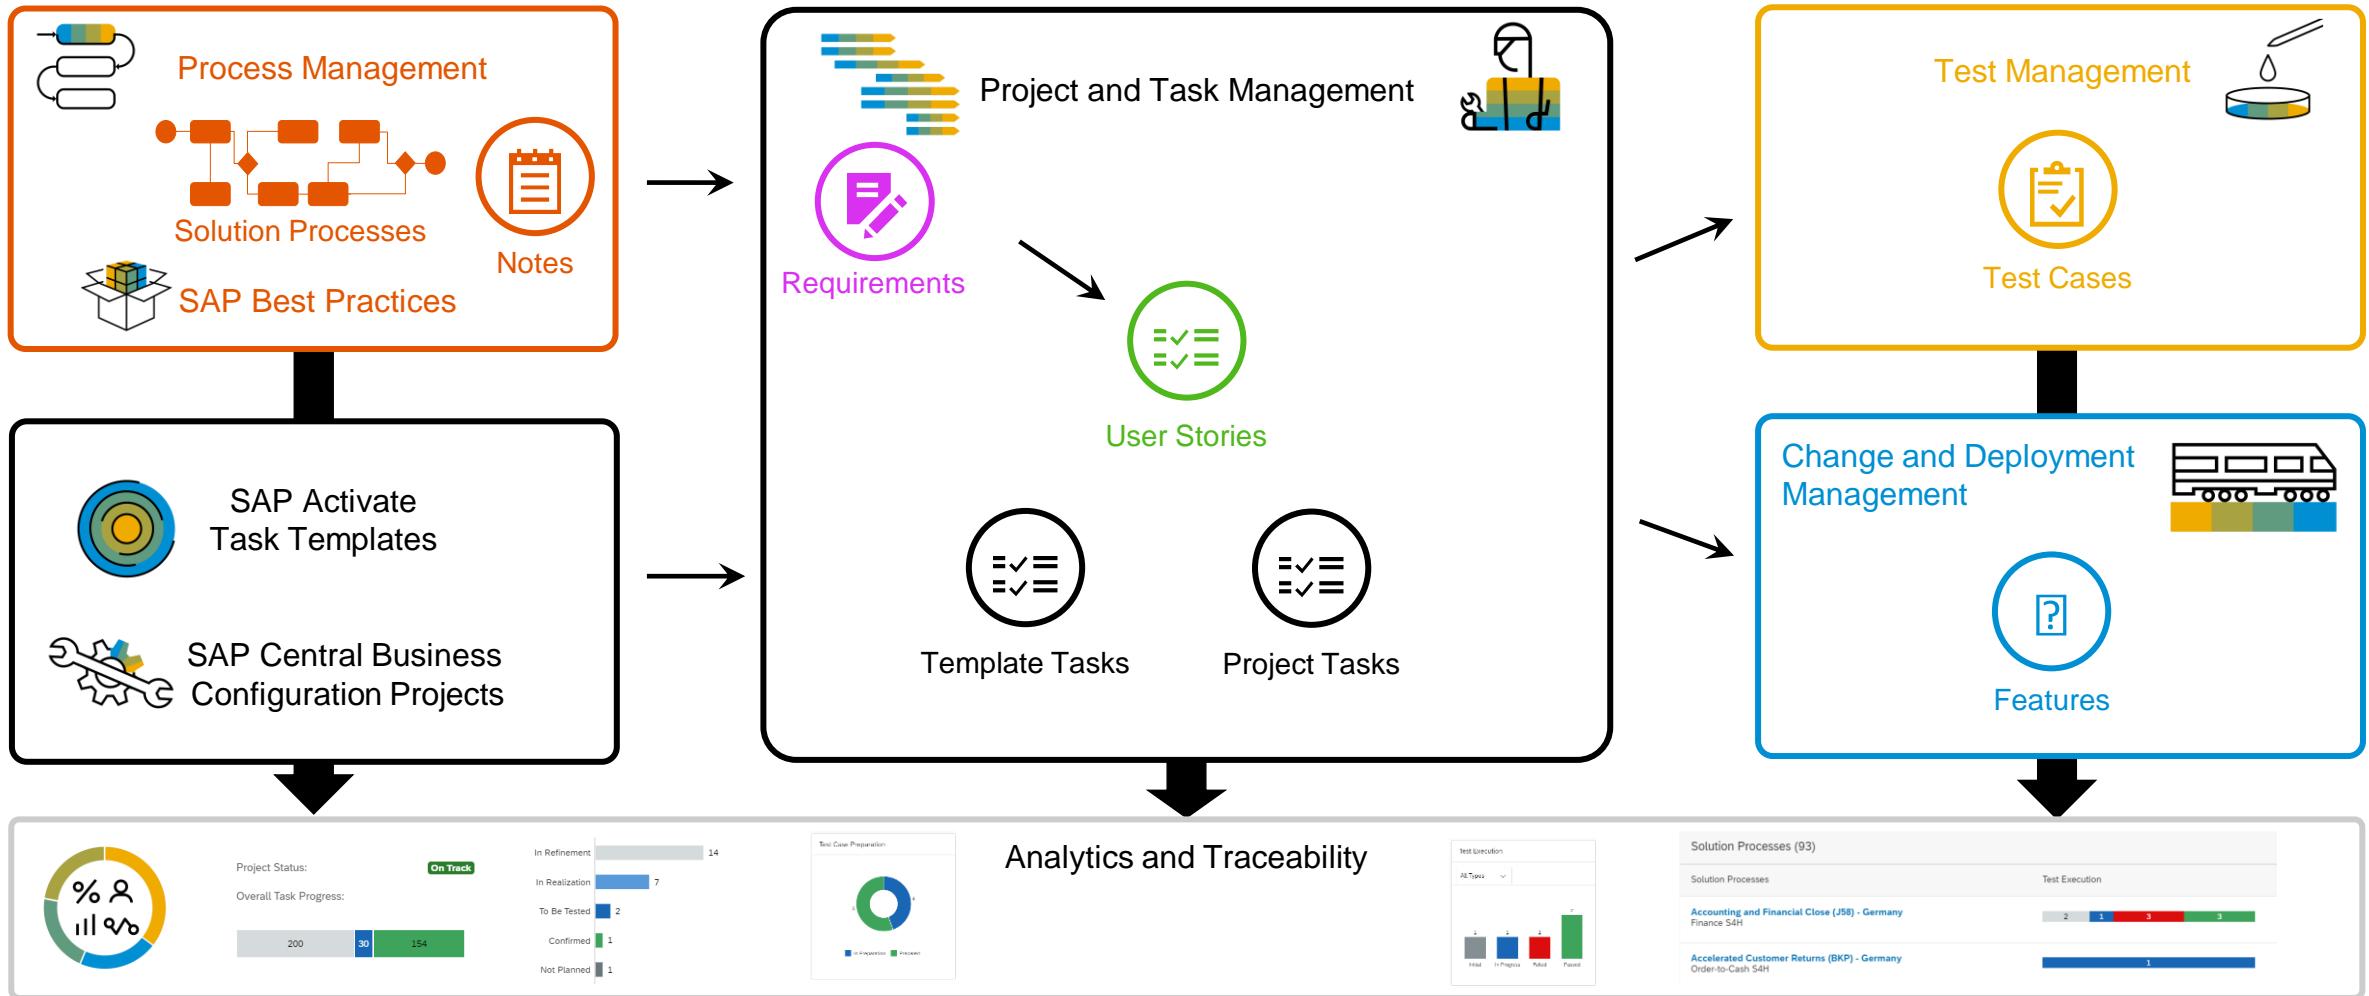

SAP Cloud ALM Entities

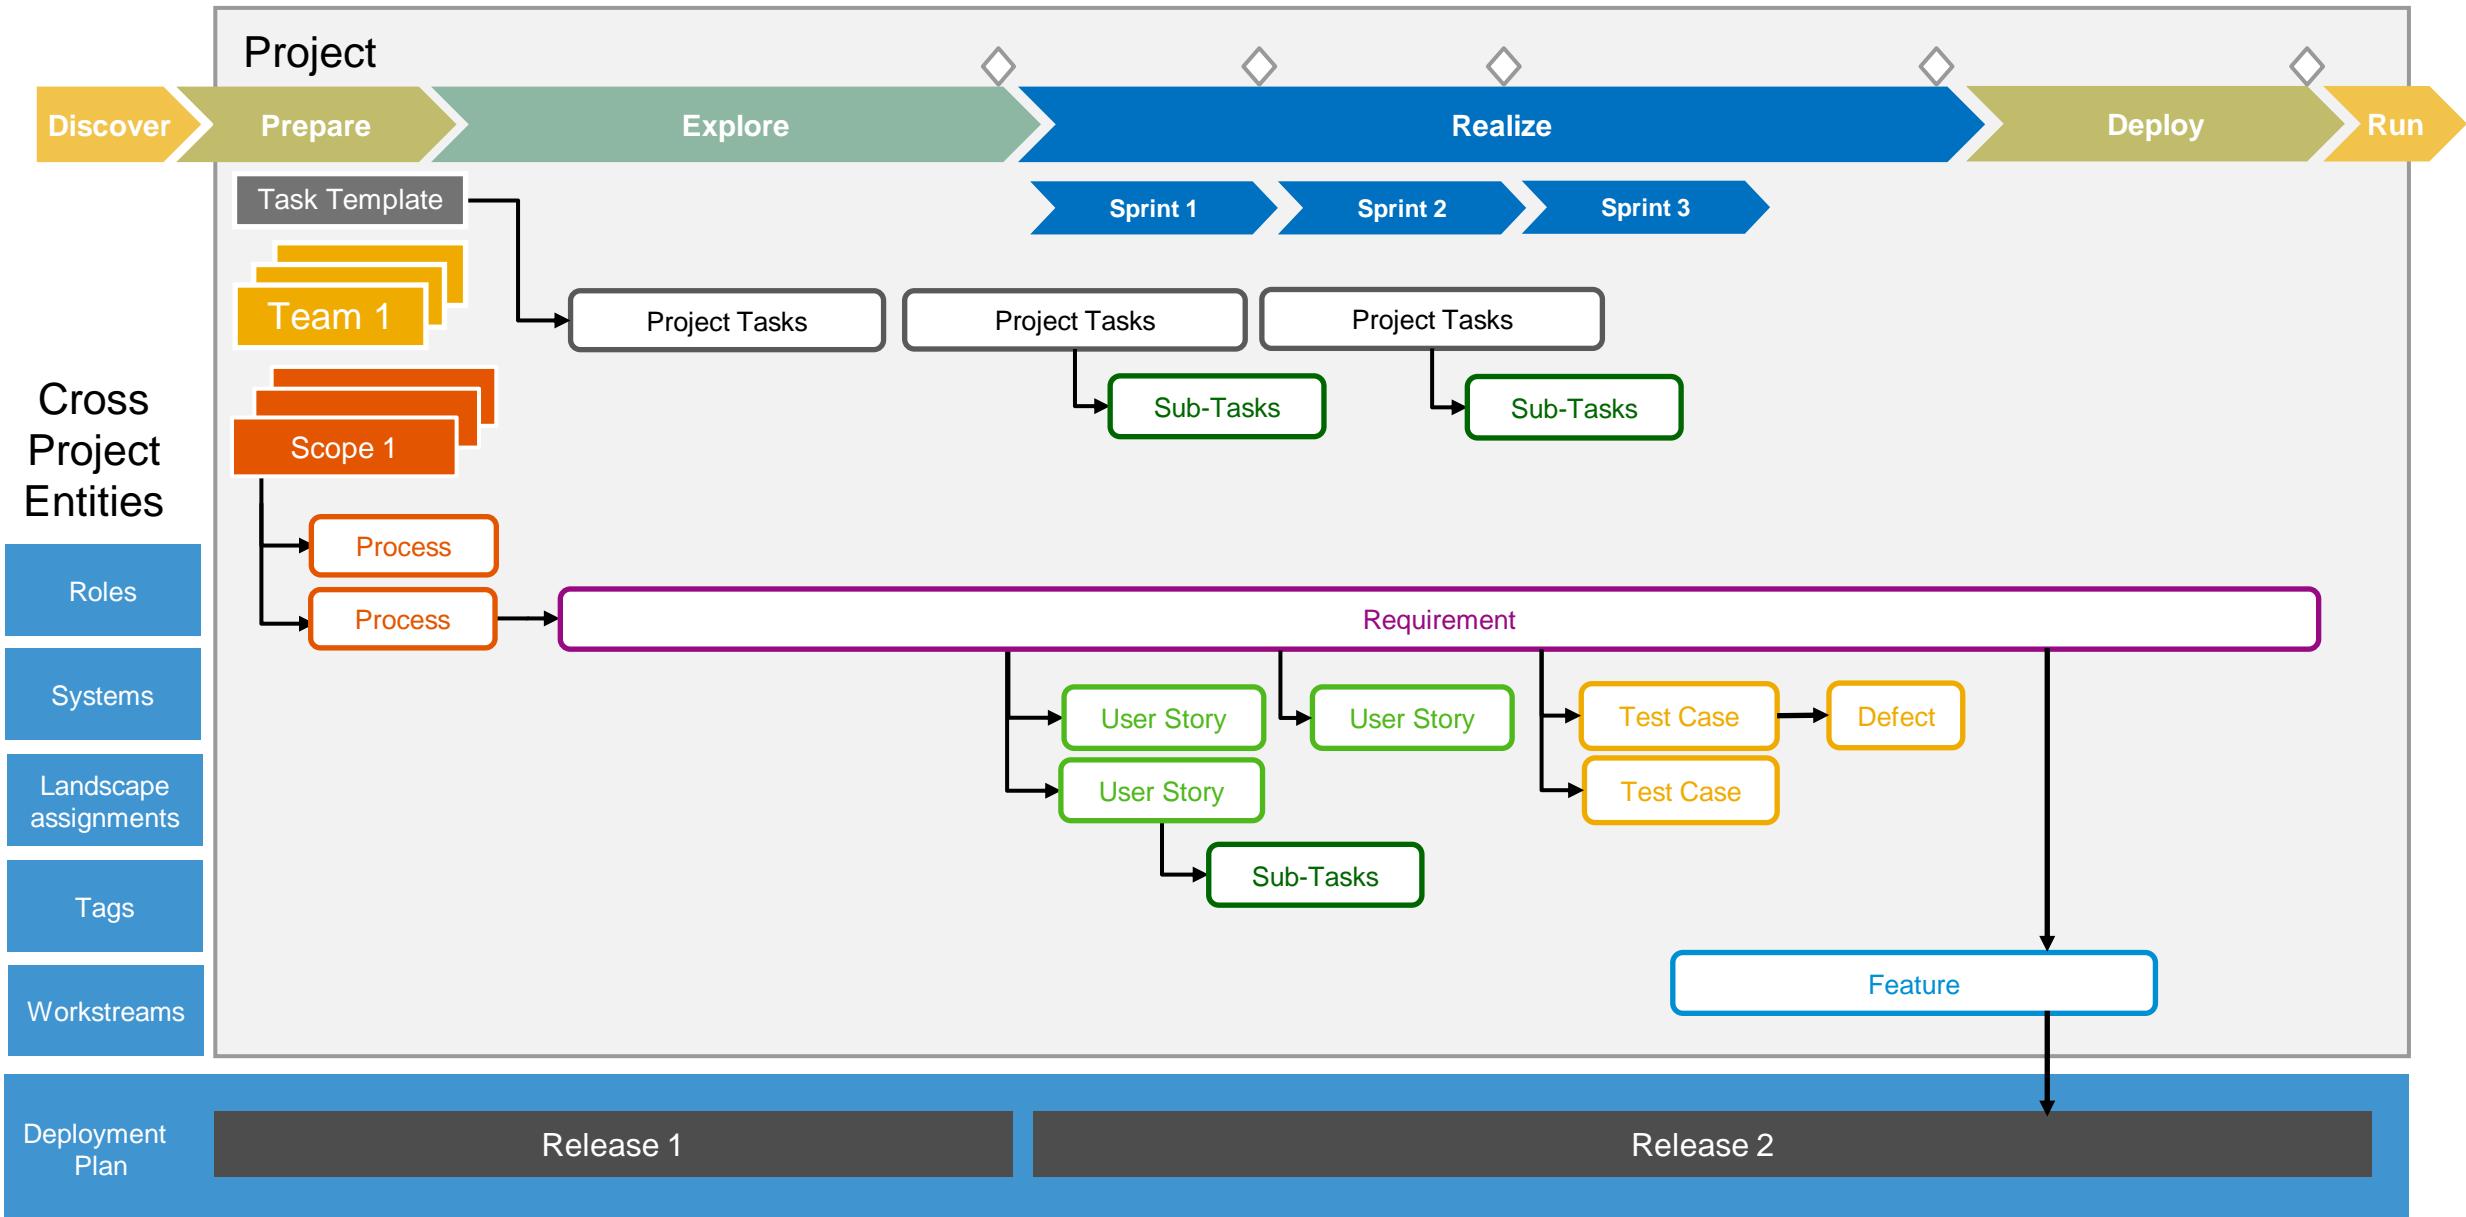


Analytics and Traceability

Overview Page

- Central entry for project manager and member
- Aggregated and organized view on all aspects of the project in one location
- Allows user specific view on project status and related activities


Analytics

- Advanced analytics
- Traceability views for E2E implementation process governance
- Various charts to track progress of
 - Task execution
 - Test Execution
 - Defect Resolution

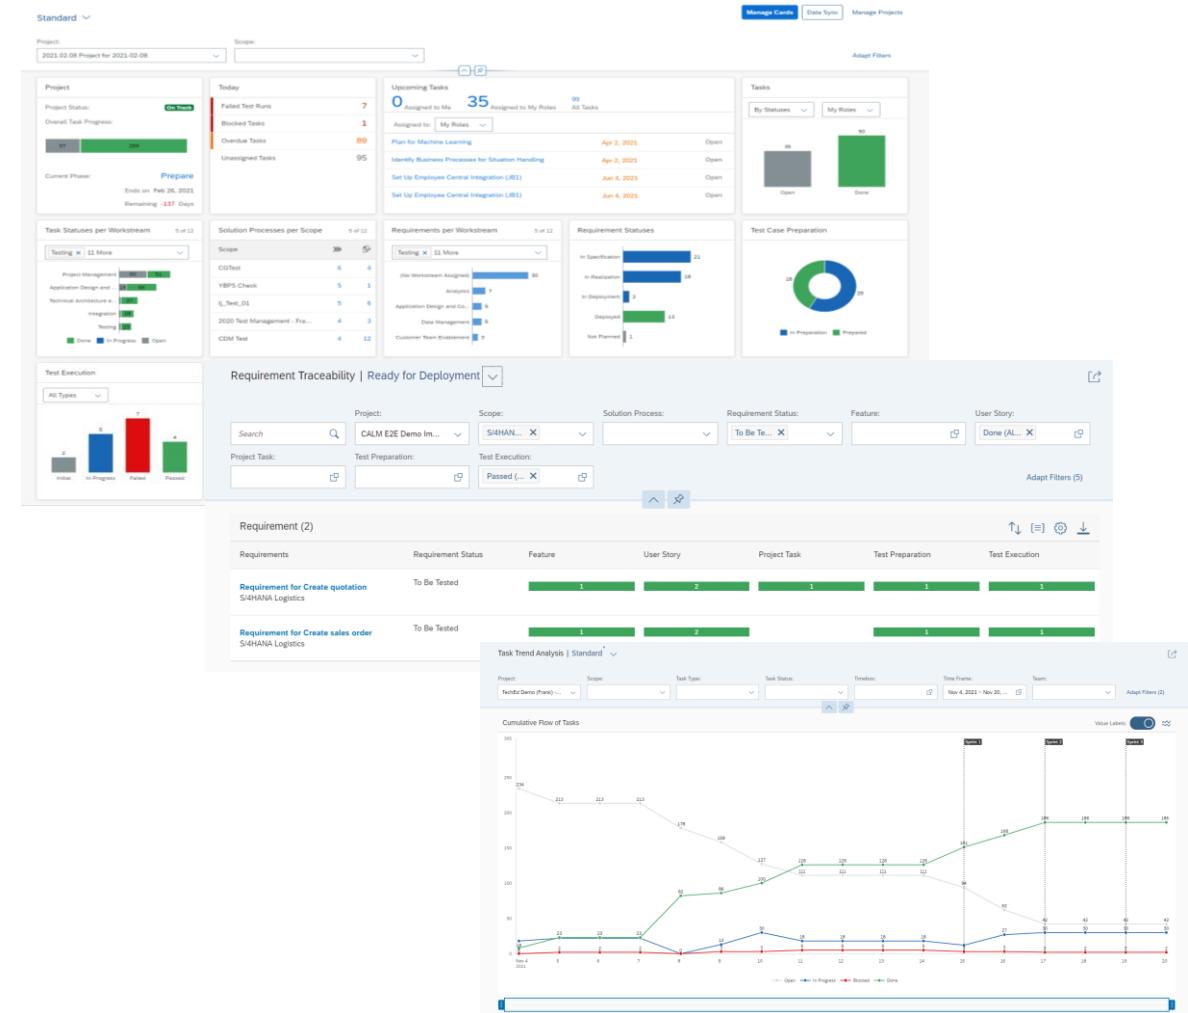


SAP Cloud ALM – Consumption of SAP Activate based roadmaps

- Implementation based on SAP Activate Methodology
- Tasks automatically assigned to roles
- Set detailed due dates or derive from phases
- Mass change of task attributes
- Creation of manual tasks
- List and Gantt view

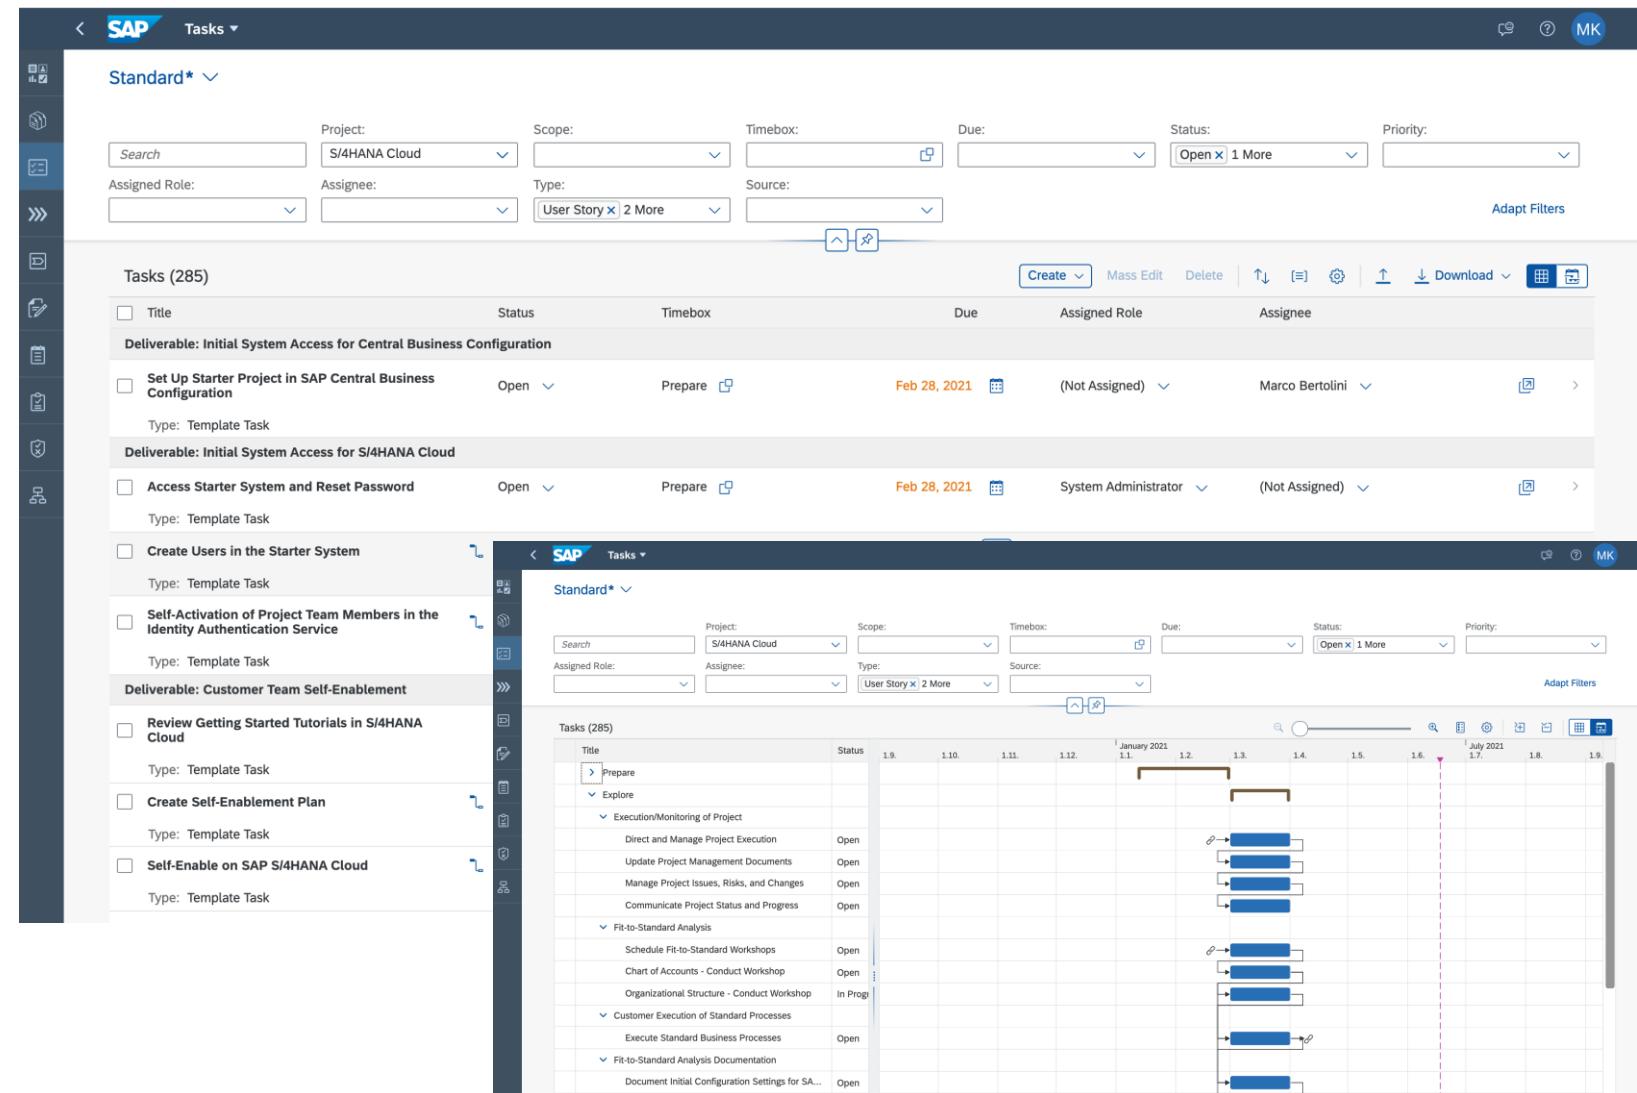

SAP Cloud ALM – Process Content Viewer for SAP Best Practice Content

- Implementation based on SAP Best Practice Process Content and Intelligent Enterprise Scenarios
- Process Based scoping for Fit-to-Standard Workshops
- Creation of requirements on process models
- Detailed access to
 - BPMN process models
 - Test Scripts
 - Executables

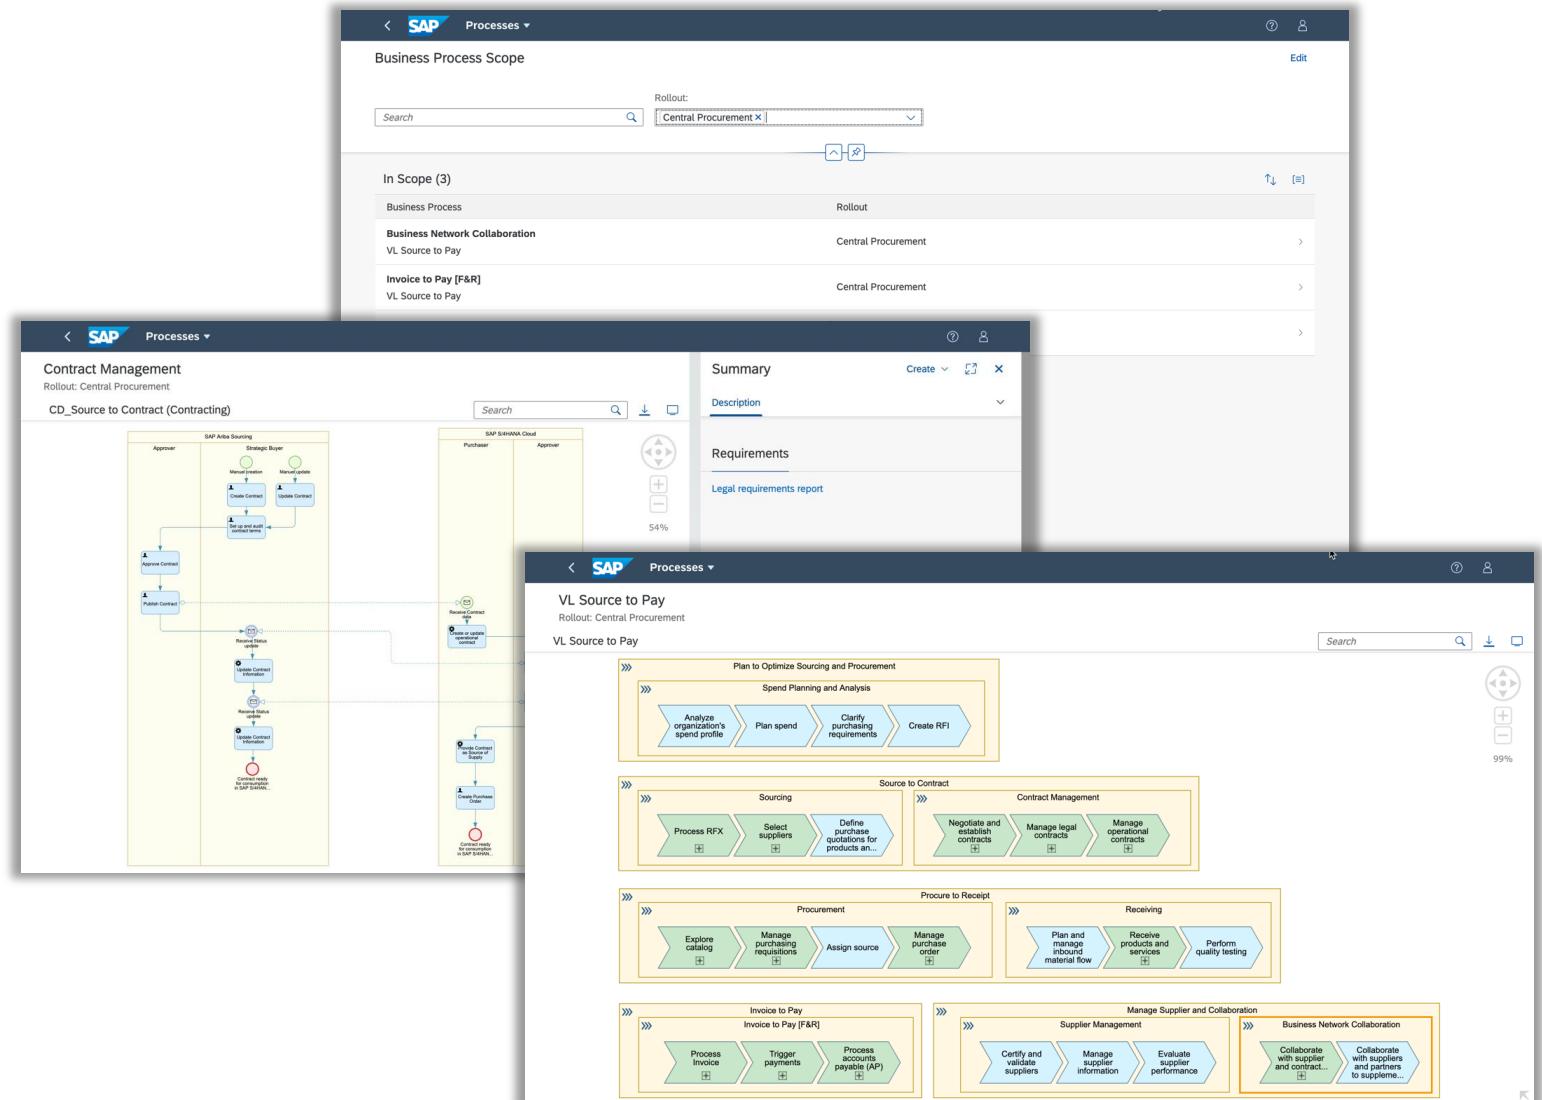

SAP Cloud ALM – Customer Content Authoring

- Create your own solution processes
- Simple versioning with draft and active versions
- Maintain Value Flow diagrams
- Use customer processes in
 - Requirements Management
 - Test Management

The image contains two screenshots of the SAP Cloud ALM interface. The top screenshot shows the 'Custom Solution Processes' screen with a search bar and a table listing one solution process: 'My first Solution Process' (Business Process Variant: 'My first Business Process'). The status is 'Active'. The bottom screenshot shows the details of 'My first Solution Process' (Draft), which is a 'Value Flow' diagram titled 'My first Business Process'. It consists of three sequential steps: 'Create Solution Process', 'Attach requirements', and 'Implement!'. The interface includes standard SAP navigation elements like a sidebar with icons and a toolbar with buttons for Activate, Edit, Detail, and Delete.

Upcoming next:

- History of changes
- Creation of solution flows with BPMN modelling

SAP Cloud ALM Test Management

Easy to consume solution.

Open to support all products in the future:


- Cloud and On-Premise
- SAP and non SAP

Test Orchestration

- Scoping
- Manual Functional Testing
- Automated Functional Testing
- Requirement Traceability

Test Automation:

- Integration of Cloud-based Test Automation providers:
 - Test automation tool for SAP S/4 HANA Cloud
 - Tricentis Test Automation for SAP*

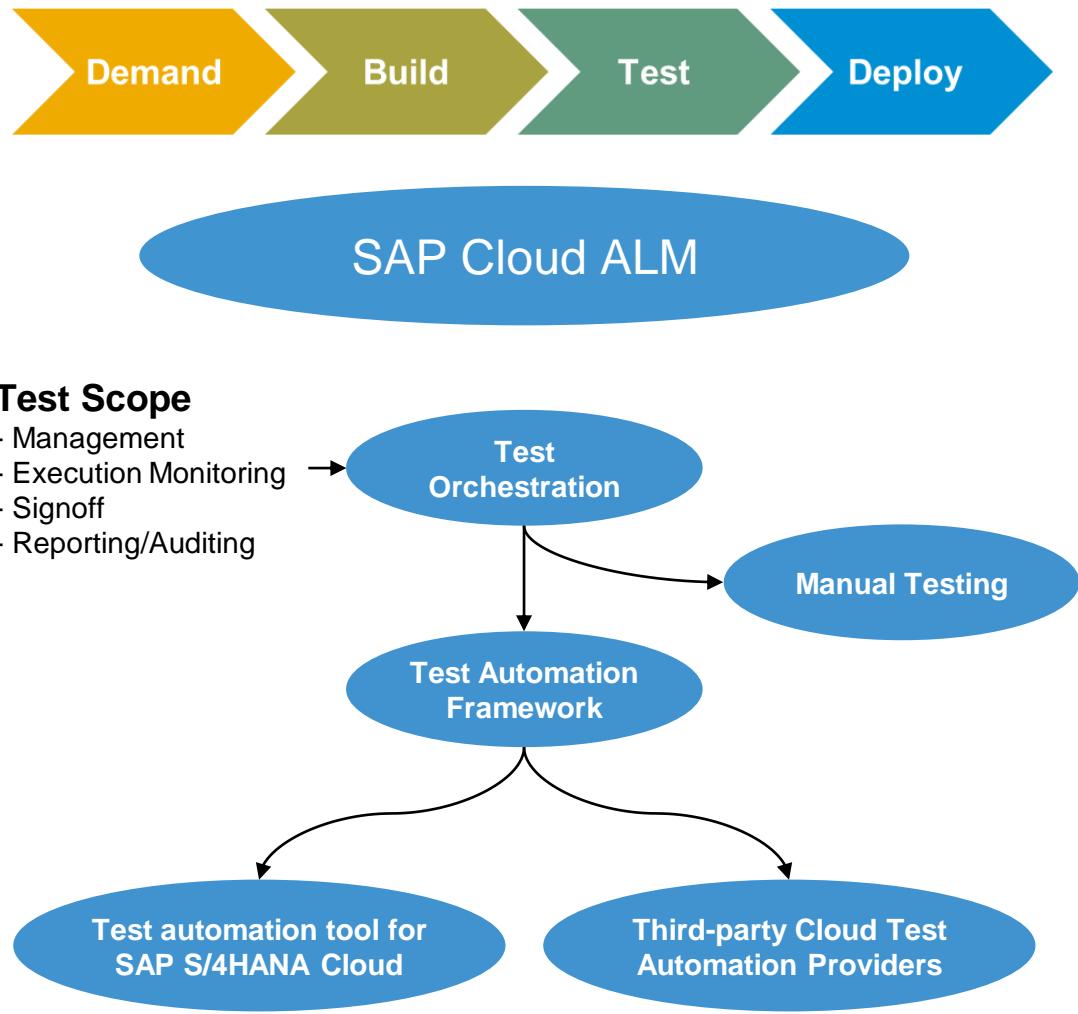

**This is the current state of planning and may be changed by SAP at any time.*

Deployment managed via Feature

- Feature is the entity for change documentation and deployment orchestration
- Easily assign transports and trigger their deployment throughout your landscape
- Traceability ensured via the history of a feature

Baseline Configuration for S/4HANA Cloud

Project: SAP @ Acron Heating Inc. Status: In Realization

Scope: Plant India Workstream: Application Design and Configuration Priority: Medium

Description Transports

Configuring the baseline for S/4HANA Cloud wrt the Activate Roadmap.

Transports

Assigned Transports (4)

ID	Title	Status	Target Tenant	Actions
J9HK900169	note for SPAU	Failed in A7R		X Deploy Assign
J9HK900448	Test for Language change	Failed in J9H~400	J9H~900	X Deploy Assign
J9HK900500	Configuration change for currency settings	Deployed in A7R~000	ZMJ~000	X Deploy Assign
J9HK900502	New sales org	Deployed in J9H~400	J9H~900	X Deploy Assign


Approve for Deployment Edit

History

Feature: Baseline Configuration for S/4HANA Cloud


- 9/24/21 at 4:26 PM Transport Request was deployed in A7R J9HK900169
- 9/24/21 at 4:26 PM Transport Request was deployed in J9H~400 J9HK900448
- 9/24/21 at 4:25 PM Transport Request was unassigned J9HK900494
- 9/24/21 at 4:25 PM Transport Request was assigned J9HK900494

Deployment integration

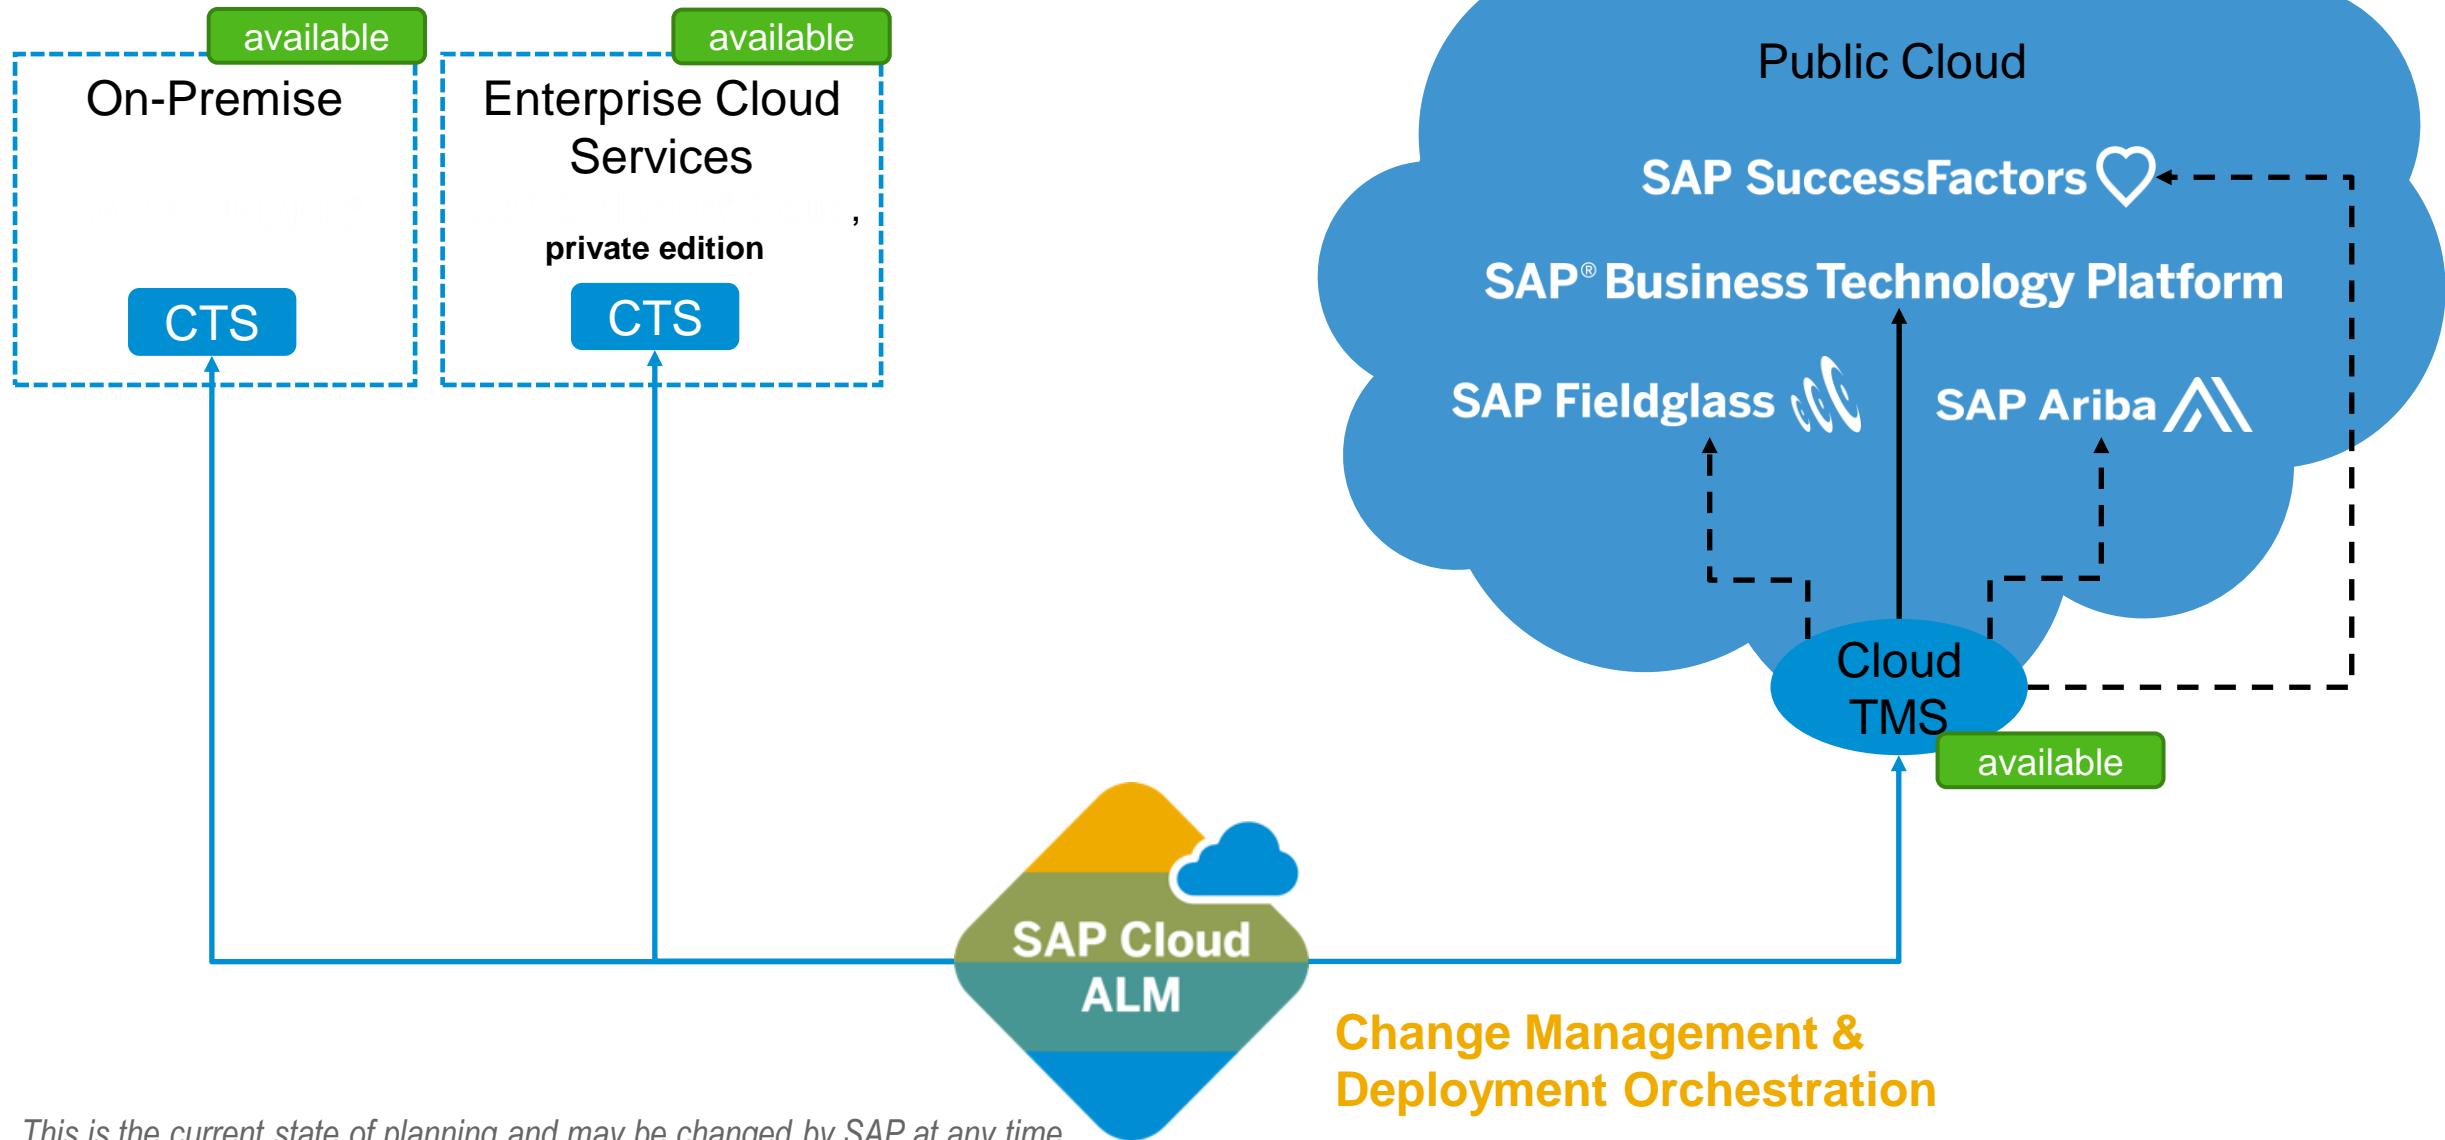


SAP Cloud ALM – Deployment Plan, Releases & Timelines


- Collective Feature deployment via Deployment Plan and Releases
- Plan Project Phases, Sprints, Milestones based on SAP Release Data
- Access to release information like ‘What’s New’ or ‘Release Impact Assessment’

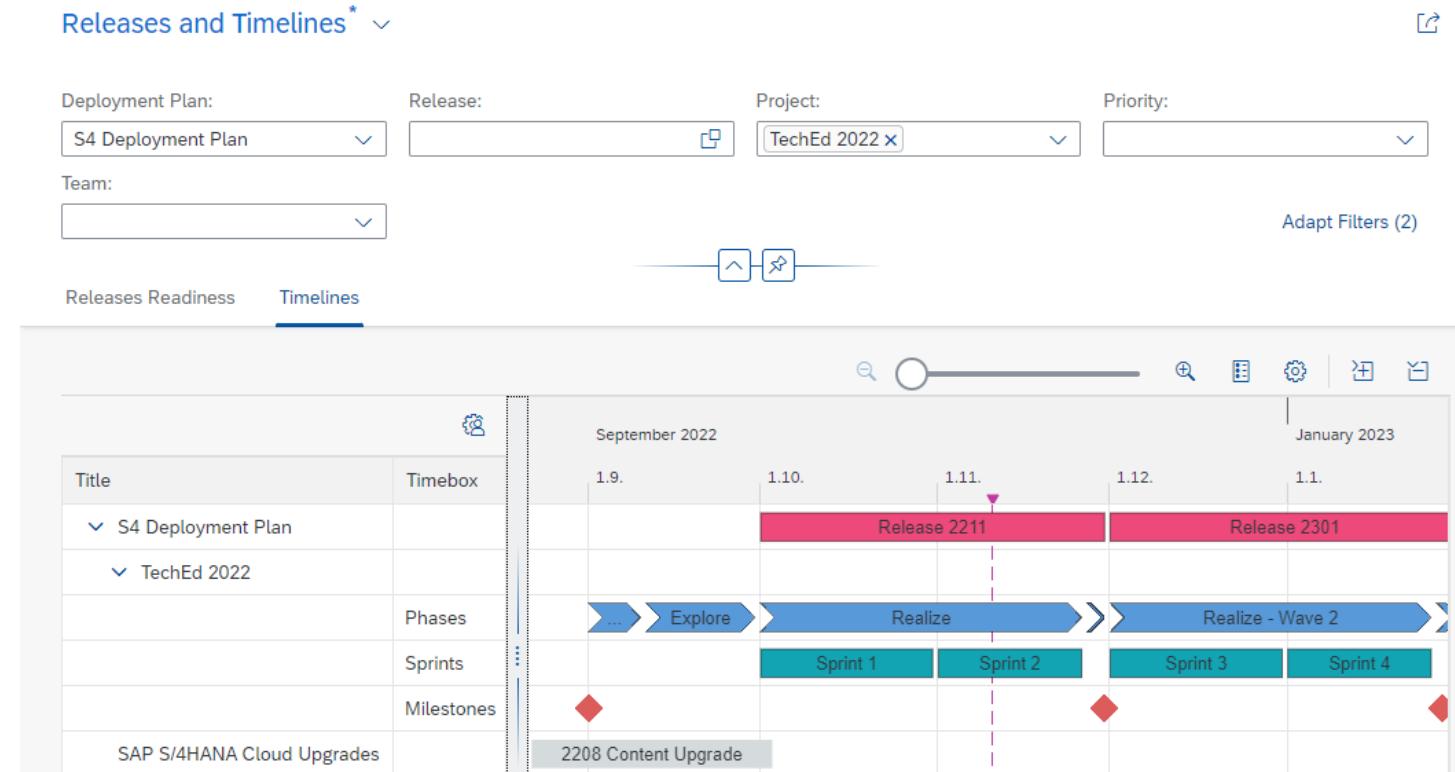

E2E Implementation Process Flow

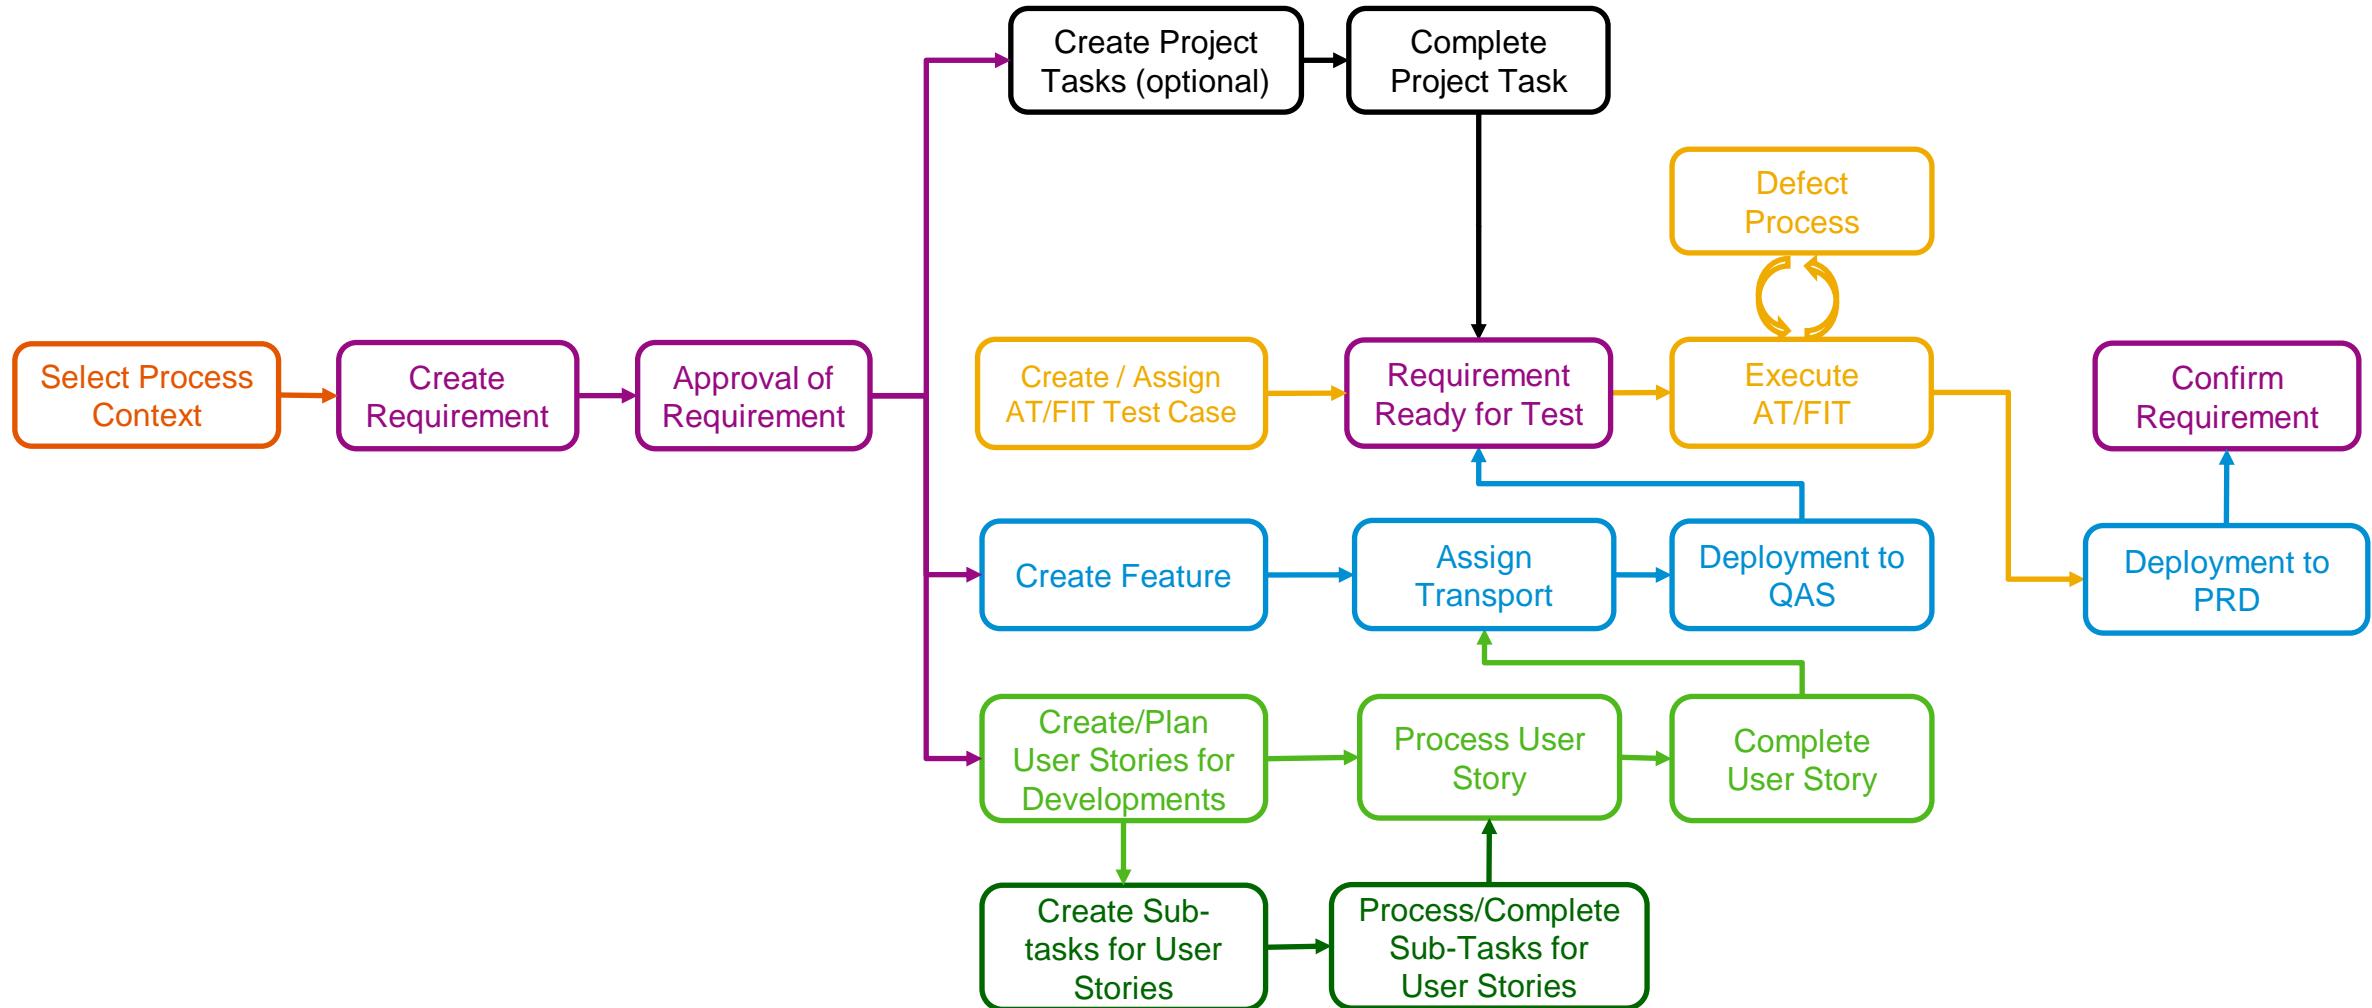

E2E Implementation Process – Requirement Ready for Implementation

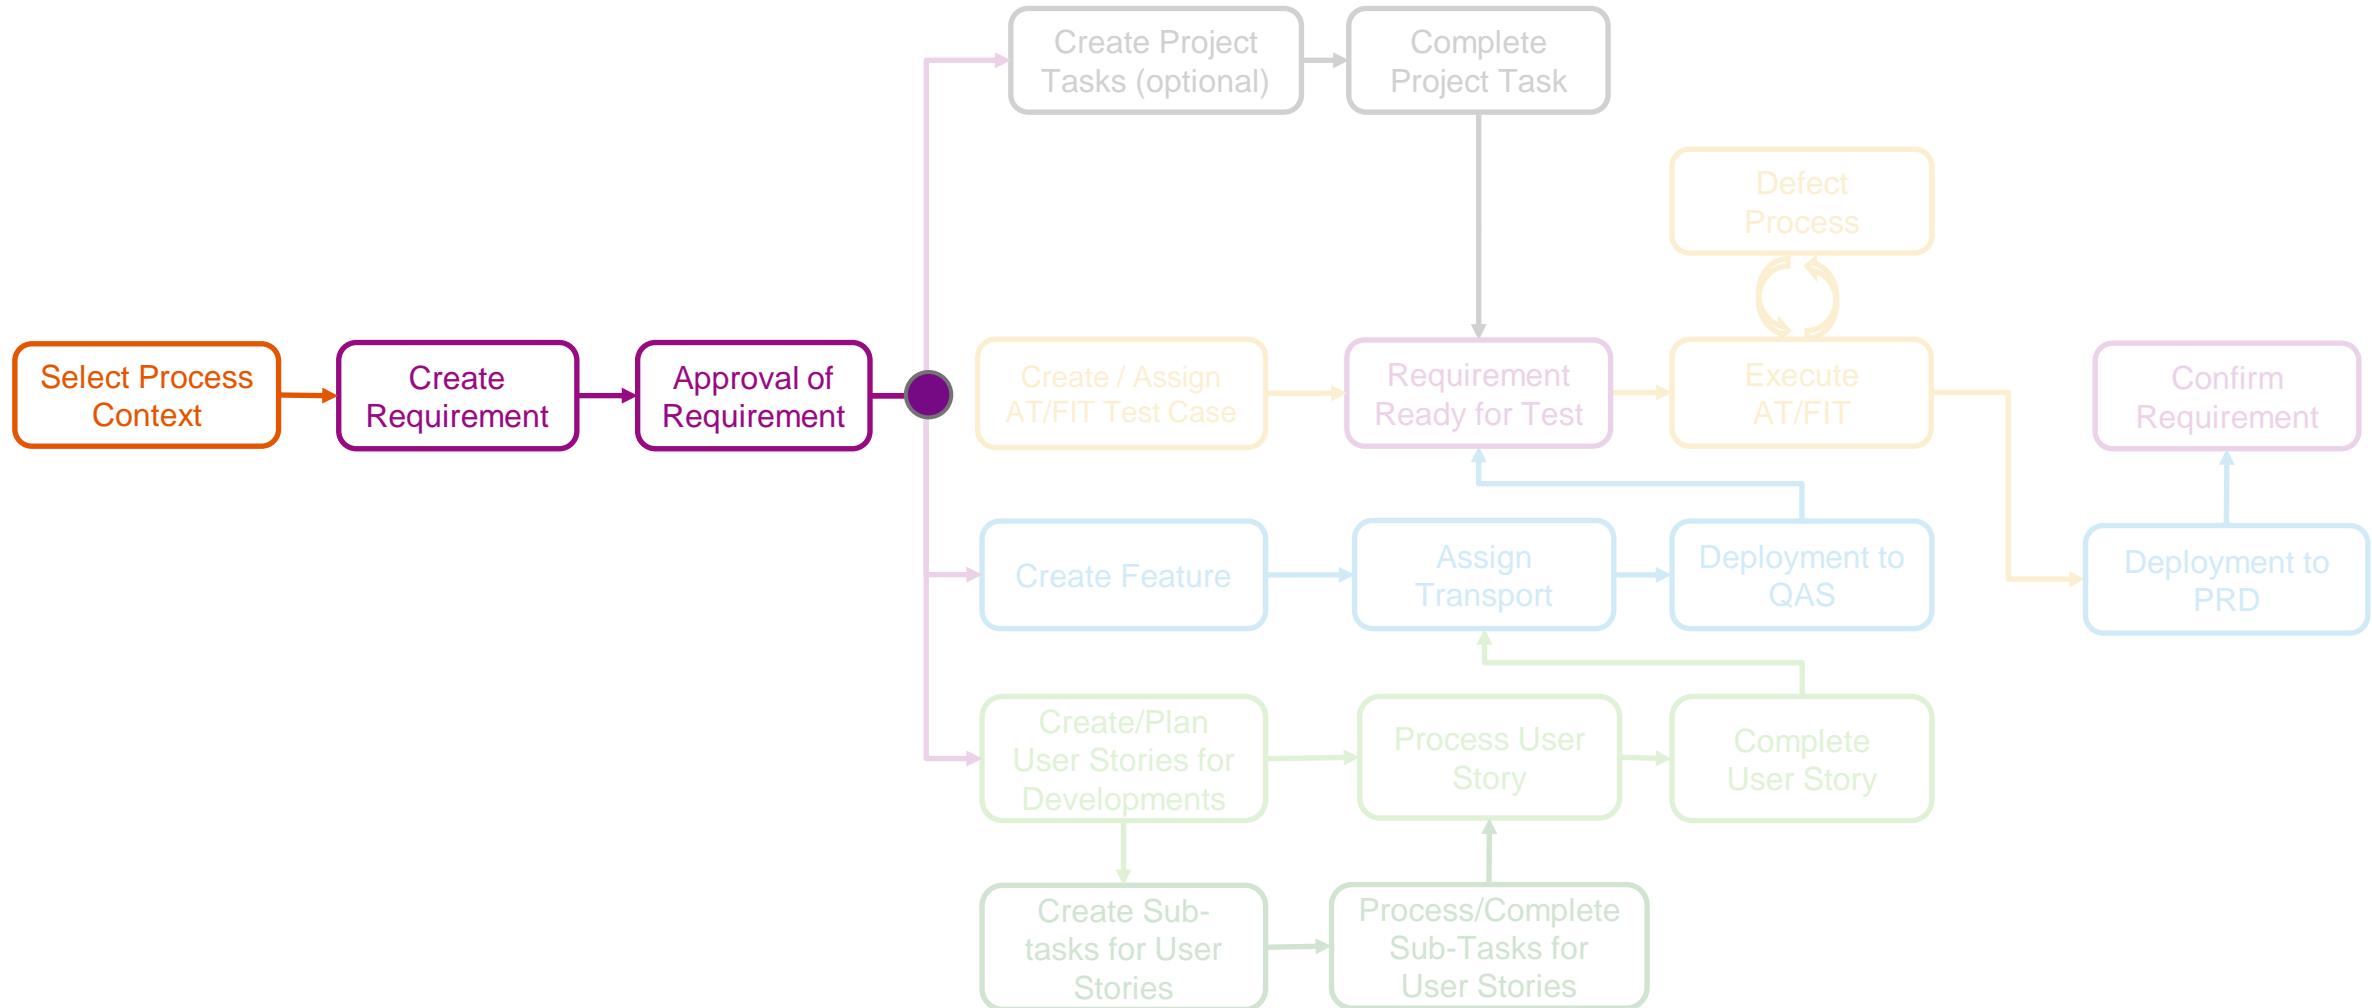

E2E Implementation Process – Requirement Ready for Implementation

Open Requirements* ▾

Project: TechEd 2022 Scope: Priority: Approval: Requirement Status:


Search TechEd 2022 ▾ Approved ▾ In Approval ▾

Team: Workstream: ▾ ▾

Items (2)

Title	Approval	Requirement Status	Priority	Solution Process	Team
<input type="checkbox"/> Requirement for Sales Quotation (BDG) S4 Sales Workstream:	Approved	In Approval ▾	= ▾	Sales Quotation (BDG)	(Not Assigned) ▾
<input type="checkbox"/> Requirement for Sell from Stock (BD9) S4 Sales	Approved	In Approval ▾	= ▾	Sell from Stock (BD9)	(Not Assigned) ▾
...					

Create ▾

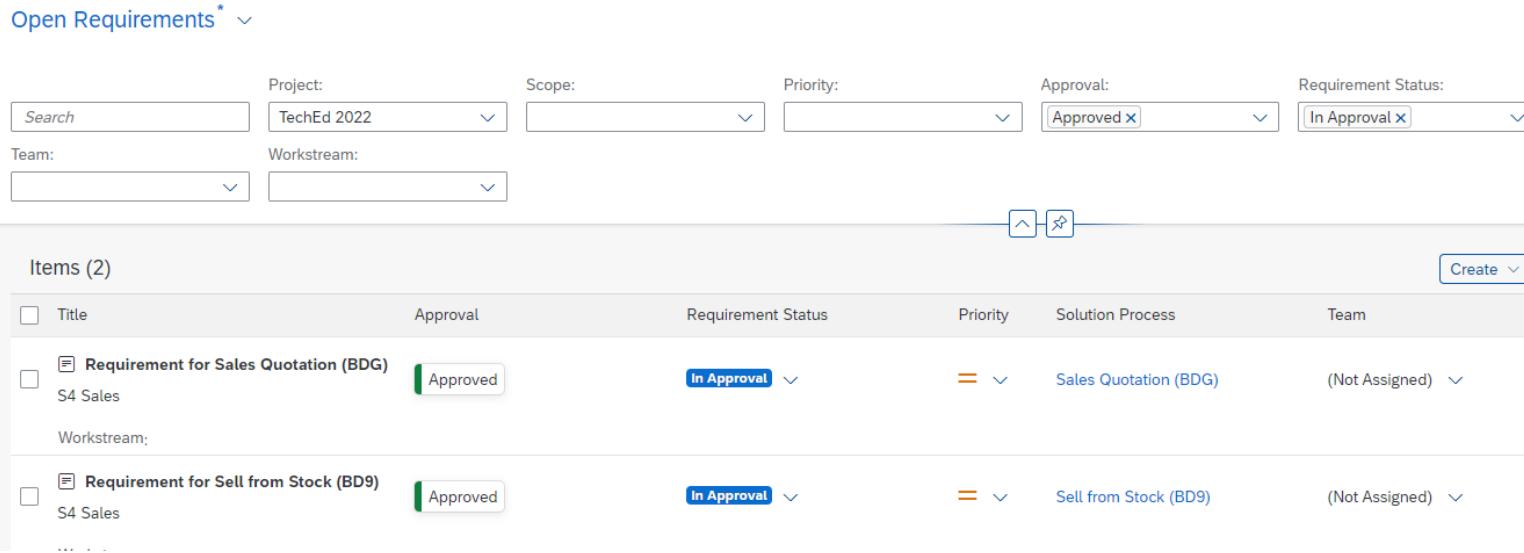


Selection Criteria

- Requirement Status = In Approval
- Approval Status = Approved

Action to be performed

- Navigate to Requirement
- Set Requirement Status to “In Realization”
- Create Feature for Requirement
- Create User Stories for Feature / Requirement
- Create/assign Test Cases

E2E Implementation Process – Requirement Ready for Test

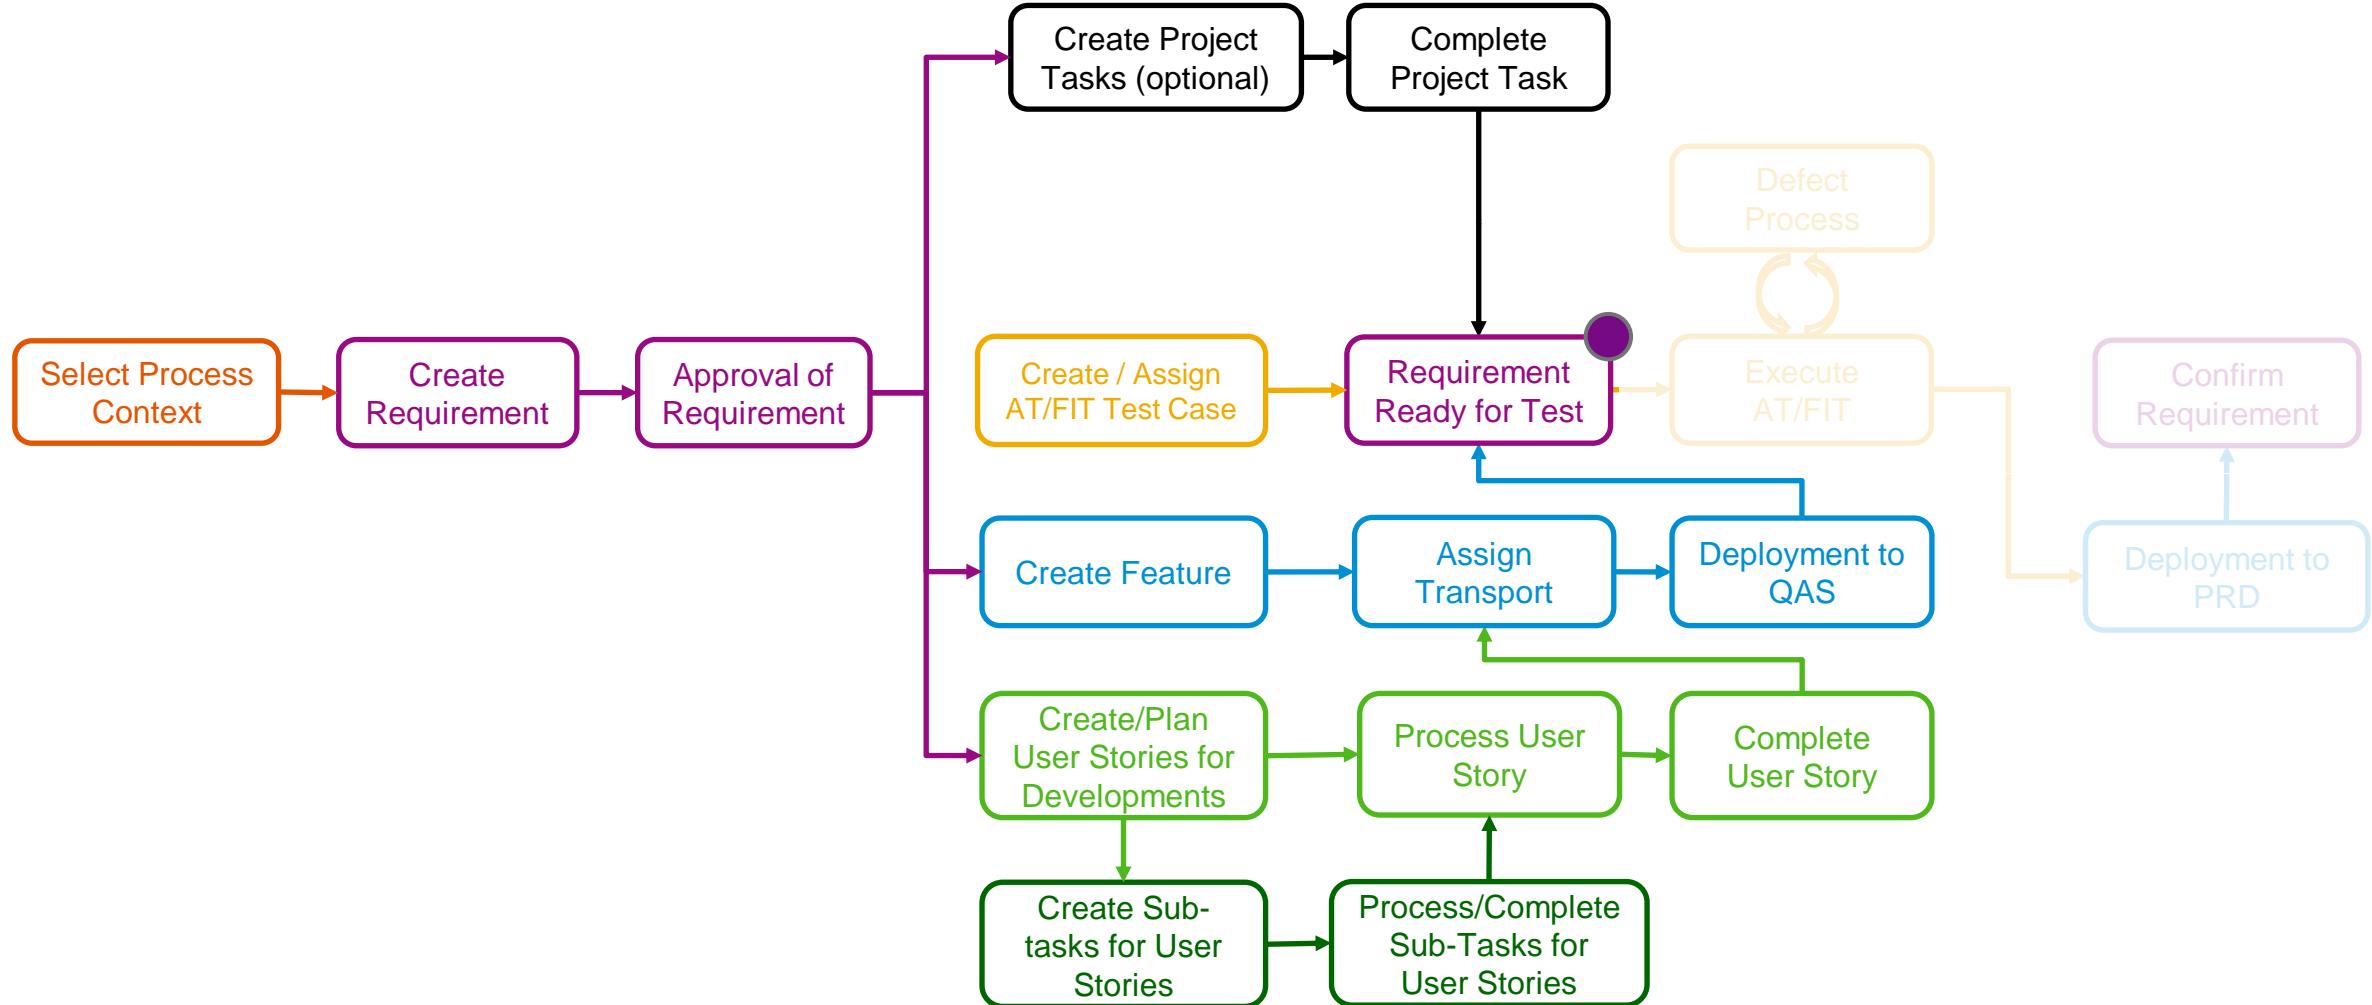

Traceability for Requirements view – Ready for Test

Requirement Traceability | Ready for Test

Project: CALM E2E Demo Implement... Scope: S/4HANA Logistics Solution Process: Requirement Status: In Realization Feature:

User Story: Done (All user st... Project Task: Prepared (All test... Test Preparation: Test Execution: Adapt Filters (5)

Requirement (2)

Requirements	Requirement Status	Feature	User Story	Project Task	Test Preparation	Test Execution
Requirement for Create quotation S/4HANA Logistics	In Realization	1	2	1	1	1
Requirement for Create sales order S/4HANA Logistics	In Realization	1	2		1	1


Selection Criteria

- Requirement Status = In Realization
- Test Preparation = All test cases with same status: Prepared
- User Story Status = All user stories with same status: Done

Action to be performed

- Navigate to Feature and deploy to QAS
- Set Requirement Status “To Be Tested”
- Start test execution

E2E Implementation Process – Ready for Deployment

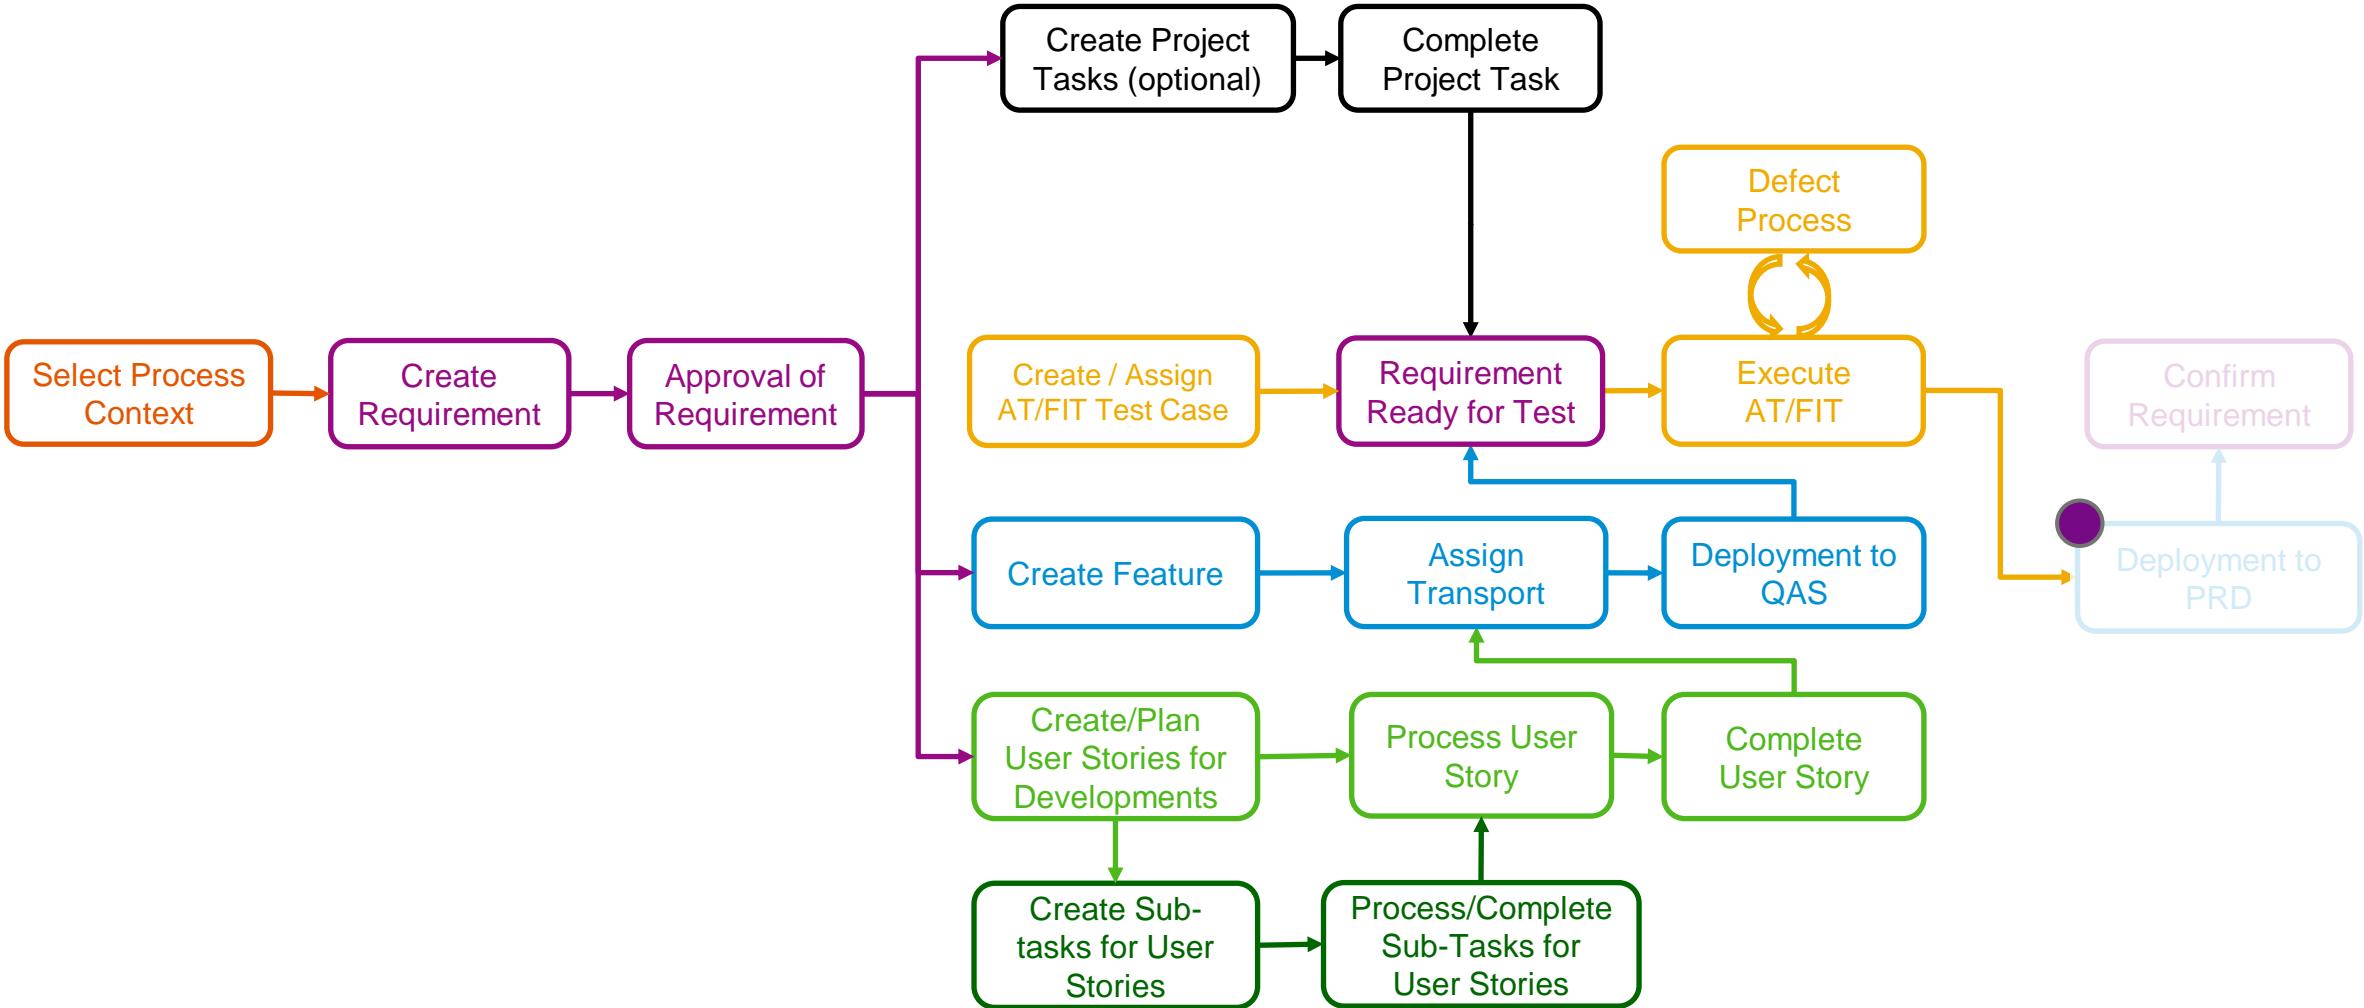

Traceability for Requirements – Ready for Deployment

Requirement Traceability | Ready for Deployment

Project: CALM E2E Demo Implement... Scope: S/4HANA Logistics Solution Process: Requirement Status: To Be Tested Feature:

User Story: Done (All user st... Project Task: Test Preparation: Test Execution: Passed (All test e... Adapt Filters (5)

Requirement (2)

Requirements	Requirement Status	Feature	User Story	Project Task	Test Preparation	Test Execution
Requirement for Create quotation S/4HANA Logistics	To Be Tested	1	2	1	1	1
Requirement for Create sales order S/4HANA Logistics	To Be Tested	1	2		1	1

Selection Criteria

- Requirement Status = To Be Tested
- Test Execution Status = All test cases with same status: Passed (only one feature)
- User Story Status = All user stories with same status: Done

Action to be performed

- Navigate to feature of requirement to set status to “Ready for Deployment”



Demo


SAP Cloud ALM Implementation & Analytics



Exercise

SAP Cloud ALM Analytics & Traceability

Additional Information

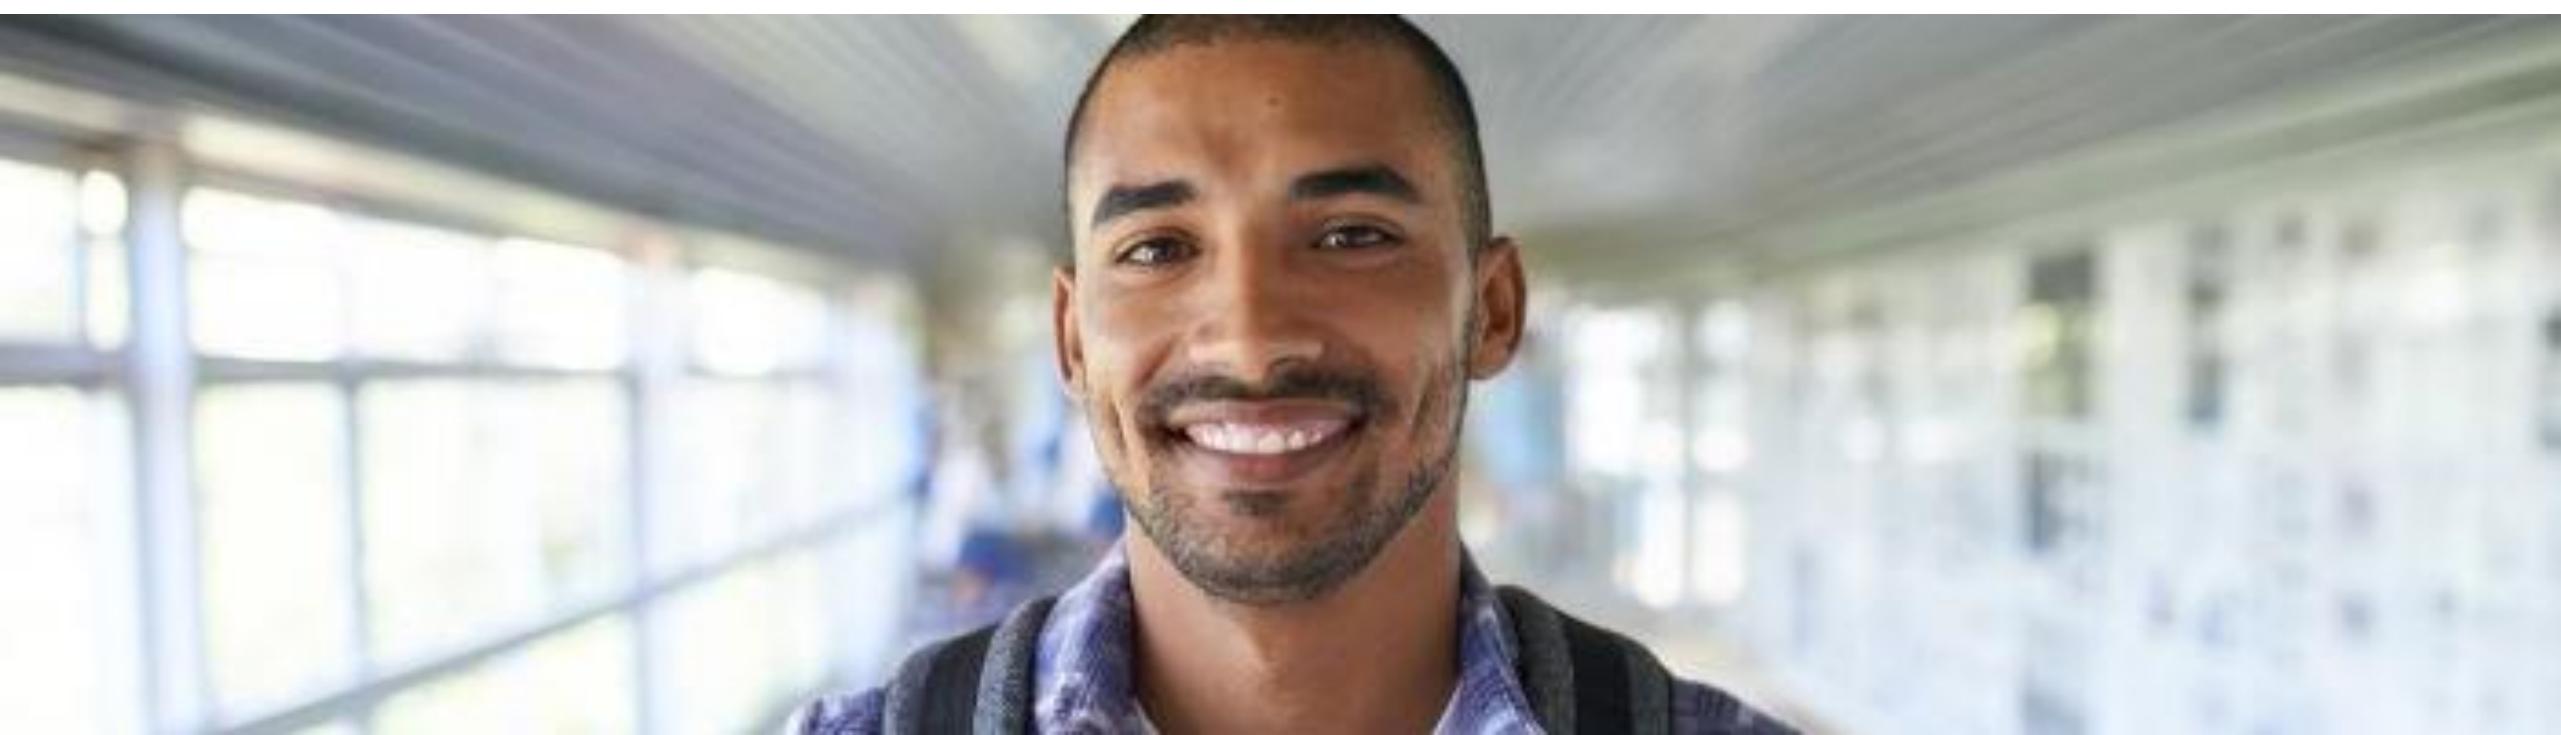

Focused Build learning material

Focused Build in SAP Solution Manager
Agile project lifecycle management

David Birkenbach, SAP
August, 2018
PUBLIC

THE BEST RUN SAP

Benefits of Project Management in Focused Build

Project Management in Focused Build offers you the following benefits

- Building the bridge between PMO team and functional teams
- Integrated project management that allows agile and classical methods for implementation projects
- Full transparency about progress, risks, issues, due dates, test results via dashboards
- Preconfigured project templates to jump start requirements-to-deploy project
- Project Management covers the complete range from planning to execution up to the project end ...Excel free

SAP's solution with Project Management helps you to manage your projects successfully. It ensures that you do things right, fast, efficient, and Excel free with preconfigured project templates, integrated tools, and reliable project management functions in SAP Solution Manager.

Launchpad and Tasks with FB for Project Manager

Project roles: Program or Project Manager, PMO, TQM, Project Team Lead

Responsibilities:

- The Project Manager is responsible for the overall management of implementation solution projects throughout its lifecycle Ex. S4HANA
- Participate in the initial planning phase and manage the execution of projects according to plan
- Proactively identify changes in work scope and ensure appropriate planning measures are taken with internal and external stakeholders to reassess and amend the scope of work requirements, budget and timeline
- Manage the financial aspects of the project budgeting and estimate to actual reporting
- Analyze the project status and identify high priority events and responsibilities for initiating mitigating action
- Ensure proper use of project management methodologies, standards, tools, processes and procedures
- Coach to clarify assignments and deliverables to project team; review quality of work and manage integration of team members' work; provide performance input to project team members' functional management
- Monitor the status of the project and distribute information accordingly to respective team members
- Perform controlling tasks including reporting/statistics

Tasks:

- Cross phase
 - * Check Q-Gate for Explore Phase Completed
 - * Manage Risk and Issues
- Prepare
 - * Project planning
 - * Create baseline build plan

FB Output

- Project Plan
- Release, Wave and Sprint details
- Optionally: Tasks, Risks and Issues

© 2018 SAP SE or an SAP affiliate company. All rights reserved. | PUBLIC | 4

Focused Build Introduction

- [Overview](#)
- [How to get started](#)
- [Release notes](#)

Functional & Conceptual overviews

- [S/4HANA Conversion Project Support](#)
- [Deployment and Release](#)
- [Project Management](#)
- [Process Management](#)
- ...

Role-based usage training material

- [Role-specific training curriculum](#)
- [Cloud trial system](#)
- [Role-specific demos in media center](#)
- [Free openSAP training](#)

Join Focused Build communities

- Access rollout material and join discussion forums about SAP Solution Manager 7.2 and focused solutions
 - [SAP Support Portal](#)
 - [Focused Solutions Wiki and FAQs](#)
- Should you have other questions, you can contact us at focused.solutions@sap.com
- Use the tag “[Focused Build and Focused Insights for SAP Solution Manager](#)” in SAP Community Network to exchange experiences or raise questions about Focused Build

The screenshot shows the SAP Support Portal homepage with a navigation bar at the top. The main content area is titled "Focused Build for SAP Solution Manager". It features a sub-headline "Manage requirements and software development in large, agile innovation projects.", a descriptive paragraph about innovating business processes, and a photograph of several people working in an office environment. Below this, there's a "Products" section with tabs for "Why Focused Build?", "Product Capabilities", "Get Focused Build" (which is selected), and "Related Products". Under "Get Focused Build", there are two sections: "Premium engagement customers" (with a link to a dedicated service) and "Non-premium engagement customers" (with a link to the SAP Store). At the bottom, there's a "News and Updates" section with a photograph of people working and a link to the Focused Build 2.0 with SP02 Release.


Additional Information SAP Cloud ALM



[Find out more](#)



[Learn what's new](#)




[See what's planned](#)



[Experience it](#)



[Request it](#)



[Get help](#)



Give feedback
(Qualtrics)



[Contact us](#)

Q&A



Open new career opportunities

Join the community of people with skills for the future



Check learning.sap.com/teched
to benefit like other certified experts:

61%
Get promotions¹

91% Increase
confidence in abilities¹

>71% Increase
problem-solving skills²



Become an SAP solution expert –
now as easy as 1,2,3 in one place:

- Follow expert-led **learning journeys and live sessions** for various development roles to upskill and **prepare for certification**
- Benefit from the **event-exclusive certification offer**



Expand your
conference experience:

- Connect with experts, share your knowledge, expand your network, and collaborate with peers in **SAP Community**
- Network with other participants in the group for **SAP TechEd** and join the **SAP Learning Groups** to get your learning questions answered



1. Pearson VUE's Latest "Value of IT Certification" Study Highlights Benefits of IT Certification in Challenging Times." Pearson Education Inc., May 25, 2021.

2. Chuck Cooper, Why Get IT Certified? The Value of IT Certification: An IT Certification White Paper, IT Certification Council, March 2021.

Thank you.

Contact information:

Reiner Markheiser
reiner.markheiser@sap.com

Joerg Marenk
joerg.marenk@sap.com

